

**PROJECT STATUS**

<b>Title</b>	Environmental Management Plan for the: <ul style="list-style-type: none"> <li>Proposed Subdivision, Rezoning, Permanent Closure, Street Creation, Consolidations of various Erven in Ondangwa Extension 3 and 28, in the Ondangwa Town Planning Scheme, and the Alteration of boundaries of Ondangwa Extension 3, Oshana Region.</li> </ul>		
<b>Report Status</b>	Final		
<b>SPC Reference</b>	OND/007		
<b>Proponent</b>	Ondangwa Town Council Private Bag 2032, Ondangwa Contact Person: Rachel Naukushu Contact Number: +264 65 240 101 Email: <a href="mailto:rnaukushu@ondangwatc.org.na">rnaukushu@ondangwatc.org.na</a>		
<b>Environmental Assessment Practitioner</b>	Stubenrauch Planning Consultants P.O. Box 41404, Windhoek Contact Person: Bronwynn Basson Contact Number: +264 (61) 25 11 89 Fax Number: +264 (61) 25 21 57 Email: <a href="mailto:bronwynn@spc.com.na">bronwynn@spc.com.na</a>		
<b>Report date</b>	July 2024		
	<b>Name</b>	<b>Signature</b>	<b>Date</b>
<b>Author</b>	Elina SP Vakuwile		July 2024
<b>Contributor</b>	Ndesihafela L. Neliwa		July 2024

**LEGAL NOTICE**

This report or any portion thereof and any associated documentation remain the property of SPC until the mandator effects payment of all fees and disbursements due to SPC in terms of the SPC Conditions of Contract and Project Acceptance Form. Notwithstanding the aforesaid, any reproduction, duplication, copying, adaptation, editing, change, disclosure, publication, distribution, incorporation, modification, lending, transfer, sending, delivering, serving or broadcasting must be authorised in writing by SPC.

**CONTENTS PAGE**

**ABBREVIATIONS..... III**

**1 INTRODUCTION ..... 5**

    1.1.1 Part A Ondangwa Extension 28 ..... 5

    1.1.2 Part B Ondangwa Extension 3 ..... 5

**2 PROPOSED DEVELOPMENT ..... 7**

    2.1 DEVELOPMENT DESCRIPTION OF PART A ONDANGWA EXT 28..... 7

        2.1.1 Project Location for Part A Ondangwa Extension 28..... 7

        2.1.2 Status Quo for Part A Ondangwa Extension 28 ..... 7

        2.1.3 Ownership and Zonings for Part A Ondangwa Extension 28 ..... 10

    2.2 DEVELOPMENT DESCRIPTION OF PART B ONDANGWA EXT 3 ..... 11

        2.2.1 Project Location for Part B Ondangwa Extension 3 ..... 11

        2.2.2 Status Quo for Part B Ondangwa Extension 3 ..... 11

        2.2.3 Ownership and Zonings for Part B Ondangwa Extension 3 ..... 11

        ..... 12

    2.3 DEVELOPMENT DESCRIPTION ..... 14

**3 ROLES AND RESPONSIBILITIES ..... 43**

    3.1 COUNCILOR’S REPRESENTATIVE ..... 43

    3.2 ENVIRONMENTAL CONTROL OFFICER ..... 44

    3.3 CONTRACTOR..... 44

**4 MANAGEMENT ACTIONS ..... 45**

    4.1 ASSUMPTIONS AND LIMITATIONS ..... 45

    4.2 APPLICABLE LEGISLATION ..... 46

    4.3 PLANNING AND DESIGN PHASE ..... 51

    4.4 CONSTRUCTION PHASE ..... 52

    4.5 OPERATION AND MAINTENANCE PHASE ..... 65

    4.6 DECOMMISSIONING PHASE ..... 67

**5 CONCLUSION ..... 67**

**LIST OF TABLES**

Table 2-1: Ownership, Size and Zoning ..... 10

Table 2-2: Ownership, size and zoning..... 11

Table 3-1 Responsibilities of CR..... 43

Table 4-1: Legislation applicable to proposed development ..... 46

Table 4-2: Planning and design management actions ..... 51

Table 4-3: Construction phase management actions ..... 52

Table 4-4: Operation and maintenance management actions ..... 65

Table 4-5: Decommissioning phase management actions..... 67

**LIST OF FIGURES**

Figure 2-1: Locality map of Erven 6651, 6652, 6653 and 6654, Ondangwa Extension 28 .....8

Figure 2-2: Status Quo for Ondangwa Extension 28 .....9

Figure 2-3: Locality map for Erven 4771, 5782, 5783, 1235 and 1236, Ondangwa Extension 3 ..... 12

Figure 2-4: Status quo for Erven 4771, 5782, 5783, 1235 and 1236, Ondangwa Extension 3 13

Figure 2-5: Subdivision of Erf 6651, Ondangwa Extension 28 into Erven A/6651, B/6651 and Remainder ..... 15

Figure 2-6: Subdivision of Erf 6652, Ondangwa Extension 28 into Erven A/6652, B/6652 and Remainder ..... 16

Figure 2-7: Subdivision of Erf 6653, Ondangwa Extension 28 into Erven A/6653, B/6653 and Remainder ..... 17

Figure 2-8: Subdivision of Erf 6654, Ondangwa Extension 28 into Erven A/6654, and Remainder ..... 18

Figure 2-9: Consolidation of erven RE/6651, RE/6652, RE/6653 and RE/6654 into Erf Y ..... 19

Figure 2-10: Rezoning of Consolidated Erf Y, Ondangwa Extension 28 from Business to Street ..... 20

Figure 2-11: Consolidated Erf W ..... 21

Figure 2-12: Rezoned consolidated Erf W, Ondangwa Extension 28 ..... 22

Figure 2-13: Consolidated Erf V, Ondangwa Extension 28 ..... 23

Figure 2-14: Rezoned Consolidated Erf V ..... 24

Figure 2-15: Alteration of the boundaries of Ondangwa Extension 3 ..... 25

Figure 2-16: Subdivision of Erf 4771, Ondangwa Extension 3 into Erven A/4771, B/4771, C/4771 and Remainder ..... 27

Figure 2-17: Rezoning of Erven B/4771 and C/4771 Ondangwa Extension 3 ..... 28

Figure 2-18: Consolidated Erf Z ..... 29

Figure 2-19: Consolidated Erf X ..... 30

Figure 2-20: Subdivision of Erf 5782, Ondangwa Extension 3 into Erven A/5782, B/5782 and Remainder ..... 31

Figure 2-21: Permanent Closure of Erven B/5782 and RE/5782, Ondangwa Extension 3 as “Public Open Space” ..... 32

Figure 2-22: Rezoning of Erf B/5782 and RE/5782, Ondangwa Extension 3 ..... 33

Figure 2-23: Subdivision of Portion 4 of the Remainder of the Farm Ondangwa Town and Townlands No. 884 ..... 34

Figure 2-24: Permanent Closure of Portion A and B of the Remainder of Portion 4, Ondangwa extension 3 as Street. .... 35

Figure 2-25: Rezoning of Portion A/4 and Portion B/4, of the Farm Ondangwa Town and Townland No. 882 ..... 36

Figure 2-26: Subdivision of Erf 5783 Ondangwa Extension 3 ..... 37

Figure 2-27: Permanent Closure of Erven A/5783 and B/5783, Ondangwa Extension 3 as a “Street” ..... 38

Figure 2-28: Rezoning of Erf A/5783 and B/5783, Ondangwa Extension 3 ..... 39

Figure 2-29: Consolidated Erf S ..... 40

Figure 2-30: Alteration of the boundaries of Ondangwa Extension 3 to include Consolidated Erf V ..... 41

Figure 2-31: Consolidated Erf T ..... 42

**ABBREVIATIONS**

AIDS	Acquired Immuno-Deficiency Syndrome
EA	Environmental Assessment
ECC	Environmental Clearance Certificate
ECO	Environmental Control Officer

---

EIA	Environmental Impact Assessment
EMA	Environmental Management Act
EMP	Environmental Management Plan
GG	Government Gazette
GIS	Geographic Information System
GN	Government Notice
GPS	Global Positioning System
HIV	Human Immuno-deficiency Virus
I&APs	Interested and Affected Parties
PR	Proponent's Representative
NHCN	National Heritage Council of Namibia
Reg.	Regulation
S	Section
SPC	Stubenrauch Planning Consultants
TB	Tuberculosis

## **1 INTRODUCTION**

The Ondangwa Town Council hereinafter referred to as the proponent intends to undertake the following activities as listed in Part A and Part B:

### **1.1.1 Part A Ondangwa Extension 28**

The following activities for Part A will be undertaken as follows:

- Subdivision of Erf 6651, Ondangwa Extension 28 into Erven A, B & Remainder;
- Subdivision of Erf 6652, Ondangwa Extension 28 into Erven A, B & Remainder;
- Subdivision of Erf 6653, Ondangwa Extension 28 into Erven A, B & Remainder;
- Subdivision of Erf 6654, Ondangwa Extension 28 into Erven A & Remainder;
- Consolidation of Erven RE/6651, RE/6652, RE/6653 & RE/6654, Ondangwa Extension 28 into Consolidated Erf Y;
- Rezoning of Consolidated Erf Y, Ondangwa Extension 28 from “Business” to “Street”;
- Consolidation of Erven B/6651, B6652 & B6653, Ondangwa Extension 28 into Consolidated Erf W;
- Rezoning of Consolidated Erf W, Ondangwa Extension 28 from “Business” to “Civic”;
- Consolidation of Erven A/6651, A/6652 & A/663 Ondangwa Extension 28 into Consolidated Erf V;
- Rezoning of Consolidated Erf V from “Business” to “Civic”;
- Alternation of Boundaries of Ondangwa Extension 3 to include Consolidated Erf V;
- Inclusion of the rezonings in the next Zoning Scheme to be prepared for Ondangwa.

### **1.1.2 Part B Ondangwa Extension 3**

The following activities for Part B will be undertaken as follows:

- Subdivision of Erf 4771, Ondangwa Extension 3 into Erven A/4771, B/4771, C/4771 & Remainder;
- Rezoning of Erf B/4771, Ondangwa Extension 3 from “Business” to “Public Open Space”;
- Rezoning of Erf C/4771, Ondangwa Extension 3 from “Business” to “Civic”;
- Consolidation of Erven A/4771 and Erf 1236, Ondangwa Extension 3 into Consolidated Erf Z;
- Consolidation of Erven RE/4771 and Erf 1235, Ondangwa Extension 3 into Consolidated Erf X;
- Subdivision of Erf 5782, Ondangwa Extension 3 into Erven A/5782, B/5782 & Remainder;
- Permanent Closure of Erven B/5782 and RE/5782, Ondangwa Extension 3 as “Public Open Space”;
- Rezoning of Erf B/5782, Ondangwa Extension 3 from “Public Open Space” to “Civic”;

- **Rezoning of Erf RE/5782, Ondangwa Extension 3 from “Public Open Space” to “Street”;**
- **Subdivision of the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 into Portions A, B & Remainder;**
- **Permanent Closure of Portions A and B of the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 as “Street”;**
- **Rezoning of Portion A/4 of the Farm Ondangwa Town and Townlands No. 882 from “Street” to “Public Open Space”;**
- **Rezoning of Portion B/4 of the Farm Ondangwa Town and Townlands No. 882 from “Street” to “Civic”;**
- **Subdivision of Erf 5783, Ondangwa Extension 3 into Erven A/5783, B/5783, C/5783 and Remainder;**
- **Permanent Closure of Erven A/5783 and B/5783, Ondangwa Extension 3 as “Street”;**
- **Rezoning of Erf A/5783, Ondangwa Extension 3 from “Street” to “Public Open Space”;**
- **Rezoning of Erf B/5783, Ondangwa Extension 3 from “Street” to “Civic”;**
- **Consolidation of Erven A/5782, A/5783, A/Ptn 4 and B/4771, Ondangwa Extension 3 into Consolidated Erf S;**
- **Alternation of Boundaries of Ondangwa Extension 3 to include Consolidated Erf V;**
- **Consolidation of Erven B/5782, B/5783, B/Ptn 4 and Consolidated Erf V, Ondangwa Extension 3 into Consolidated Erf T;**
- **Inclusion of the rezonings in the next Zoning Scheme to be prepared for Ondangwa.**

The above development triggers listed activities in terms of the Environmental Management Act (No. 7 of 2007) and Environmental Impact Assessment Regulations (Government Notice No. 30 of 2012).

An Environmental Management Plan (EMP) is one of the most important outputs of the EIA process as it synthesises all the proposed mitigation and monitoring actions, set to a timeline and with specific assigned responsibilities. This EMP details the mitigation and monitoring actions to be implemented during the following phases of these developments:

- **Planning and Design** – the period, prior to construction, during which preliminary legislative and administrative arrangements, necessary for the preparation of erven, are made and engineering designs are carried out. The preparation of construction tender documents forms part of this phase;
- **Construction** – the period during which the proponent, having dealt with the necessary legislative and administrative arrangements, appoints a contractor for the development of services infrastructure and construction of the road to service the development as well as any other construction process(s) within the development areas;
- **Operation and Maintenance** – the period during which the services infrastructure will be fully functional and maintained.

It should be noted that to date, no engineering designs have been carried out for the development of the infrastructure associated with this development.

The decommissioning of these developments is not envisaged; however in the event that this should be considered some recommendations have been outlined in **Table 4-5**.

## **2 PROPOSED DEVELOPMENT**

### ***2.1 DEVELOPMENT DESCRIPTION OF PART A ONDANGWA EXT 28***

#### ***2.1.1 Project Location for Part A Ondangwa Extension 28***

The subject areas which are Erven 6651, 6652, 6653 and 6654 are located southwest of the neighbourhood Ondangwa Extension 28, as depicted in **Figure 2-1** overleaf.

#### ***2.1.2 Status Quo for Part A Ondangwa Extension 28***

As depicted in **Figure 2-2** below, the subject area is fully build up and populated with mostly business structures that are essential in the day to day lives of the residents of Ondangwa. However, most of these buildings have not been erected within the demarcated erf boundaries. Similarly, the existing road that distributes the traffic from the B1 Road into the neighbourhood of Ondangwa Extension 3 does not align with the demarcated road reserve on the layout plan for Ondangwa Extension 3, which ought to run between Erf 1236, Ondangwa Extension 3 and Erven 6652 and 6653, Ondangwa Extension 28 as depicted in the attached maps. The layout plans for Ondangwa Extension 3 and 28 thus need to be amended in order to accommodate and reflect the existing situation on the ground.

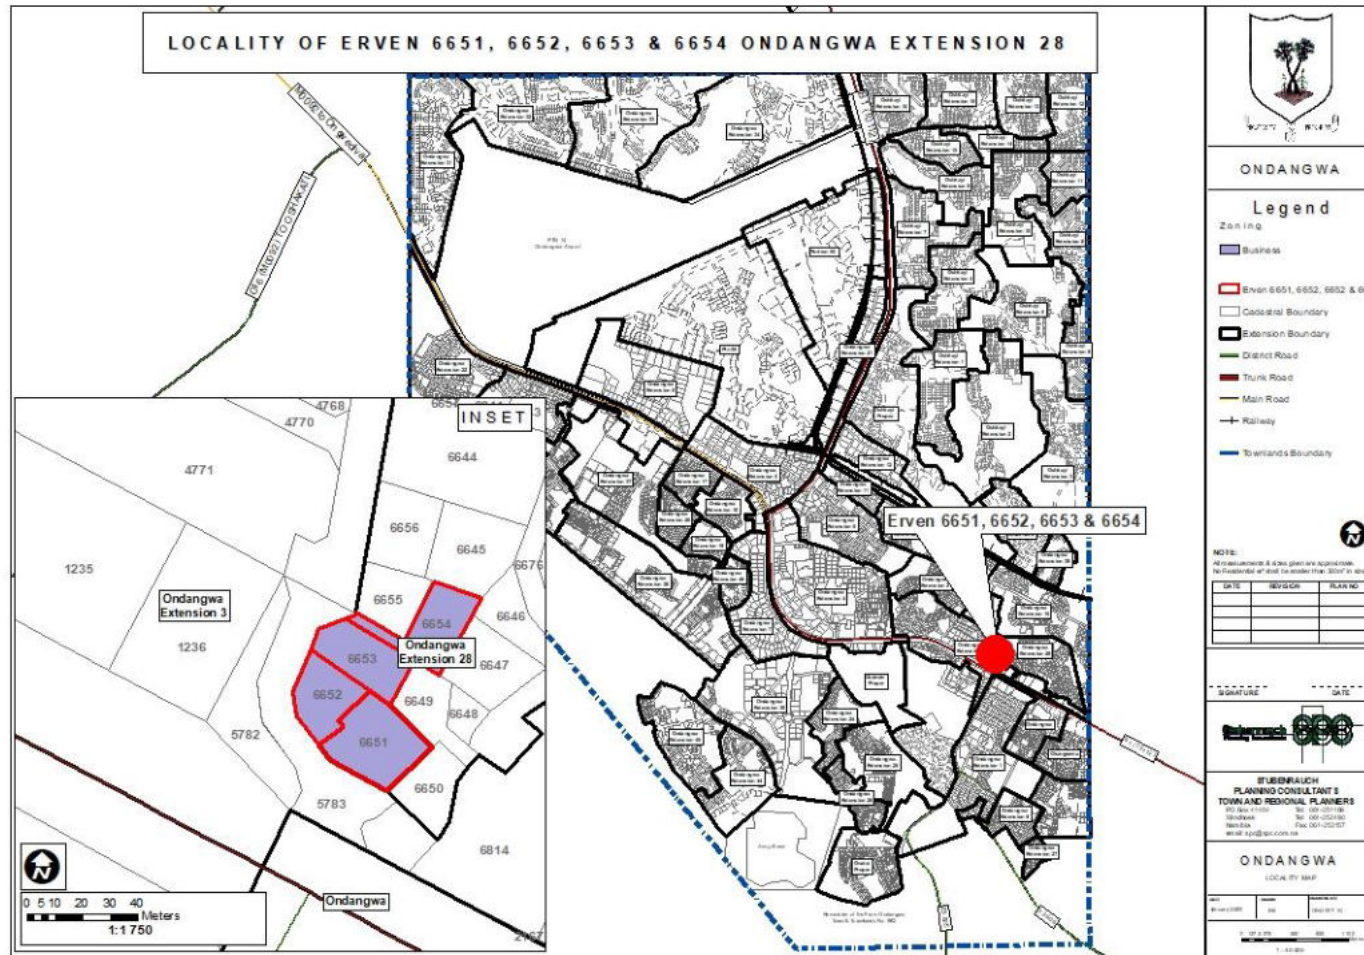


Figure 2-1: Locality map of Erven 6651, 6652, 6653 and 6654, Ondangwa Extension 28





**Figure 2-2:** Status Quo for Ondangwa Extension 28

### 2.1.3 Ownership and Zonings for Part A Ondangwa Extension 28

Ownership of the subject erven and their current zonings in terms of the Ondangwa Zoning Scheme are as is outlined in Table 2 below.

**Table 2-1:** Ownership, Size and Zoning

<b>ERF NUMBER</b>	<b>NAME OF OWNER</b>	<b>SIZE</b>	<b>CURRENT ZONING</b>
<b>Erf 6651, Ondangwa Extension 28</b>	Ondangwa Town Council (T3024/1997)	782	Business
<b>Erf 6652, Ondangwa Extension 28</b>	Ondangwa Town Council (T3024/1997)	547	Business
<b>Erf 6653, Ondangwa Extension 28</b>	Ondangwa Town Council (T3024/1997)	604	Business
<b>Erf 6654, Ondangwa Extension 28</b>	Ondangwa Town Council (T3024/1997)	611	Business

## 2.2 DEVELOPMENT DESCRIPTION OF PART B ONDANGWA EXT 3

### 2.2.1 Project Location for Part B Ondangwa Extension 3

The Erven 1235, 1236, 4771, 5782, 5783 as well as the subject area on the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 are located south of the neighbourhood of Ondangwa Extension 3 around the Huhu City Shopping Complex as depicted in the locality map **Figure 2-3** below.

### 2.2.2 Status Quo for Part B Ondangwa Extension 3

The subject area is fully built up and populated with mostly business structures that are essential in the day to day lives of the residents of Ondangwa. However, most of these buildings have not been erected within the demarcated erf boundaries. Similarly, the existing road that distributes the traffic from the B1 Road into the neighbourhood of Ondangwa Extension 3 does not align with the demarcated road reserve on the layout plan for Ondangwa Extension 3, which ought to run between Erf 1236, Ondangwa Extension 3 and Erven 6652 and 6653, Ondangwa Extension 28 as depicted in **Figure 2-4** below. The layout plans for Ondangwa Extension 3 and 28 thus need to be amended in order to accommodate and reflect the existing situation on the ground.

### 2.2.3 Ownership and Zonings for Part B Ondangwa Extension 3

Ownership of the subject erven and their current zonings in terms of the Ondangwa Zoning Scheme are as is as outlined in Table3 below:

**Table 2-2:** Ownership, size and zoning

ERF NUMBER	NAME OF OWNER	SIZE	CURRENT ZONING
Erf 5782, Ondangwa Extension 3	Ondangwa Town Council (T4017/2017)	951	Public Open Space
Erf 5783, Ondangwa Extension 3	Ondangwa Town Council (T/3024/1997)	1600	Street
Erf 1235, Ondangwa Extension 3	Paavo Mulanduleni Amwele (T310/2004)	5160	Business
Erf 1236, Ondangwa Extension 3	Iyambo Iyambo (T5360/2000)	2400	Business
Erf 4771, Ondangwa Extension 3	Ondangwa Town Council (T3024/1997)	6732	Business
The Remainder of Portion 4 of the Farm Ondangwa Townlands No. 882	Ondangwa Town Council (T3024/1997)		Street



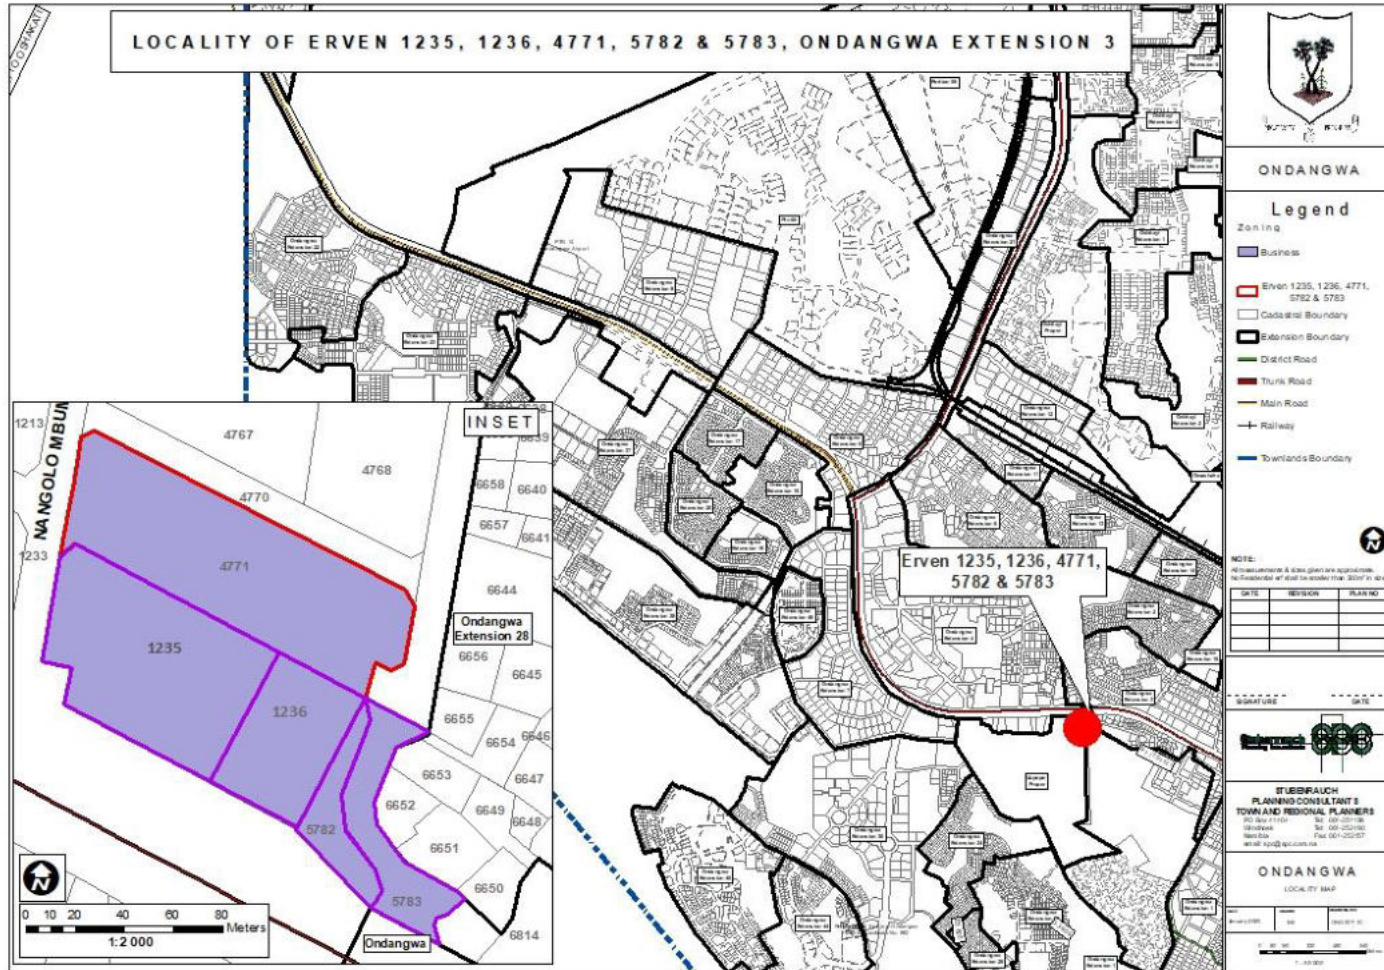


Figure 2-3: Locality map for Erven 4771, 5782, 5783, 1235 and 1236, Ondangwa Extension 3





**Figure 2-4:** Status quo for Erven 4771, 5782, 5783, 1235 and 1236, Ondangwa Extension 3

## **2.3 DEVELOPMENT DESCRIPTION**

The subject areas on Part A, which are Erven 6651, 6652, 6653, and 6654, are located southwest of the neighbourhood of Ondangwa Extension 28, while the subject areas for Part B, which are Erven 1235, 1236, 4771, 5782, and 5783, as well as the subject area on the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882, are located south of the neighbourhood of Ondangwa Extension 3 around the Huhu City Shopping Complex.

This exercise aims to amend the layout plans for Ondangwa Extension 3 and Ondangwa Extension 28 in order to accommodate and reflect the existing situation on the ground. The area to be amended or re-planned is around the Open Market and the Huhu City Shopping Complex in Ondangwa Extension 3 and Ondangwa Extension 28. This will allow the owners of the properties to have their properties rectified as per the site.

The subject areas are fully built up and populated with mostly business structures that are essential in the day to day lives of the residents of Ondangwa. However, most of these buildings have not been erected within the demarcated erf boundaries. Similarly, the existing road that distributes the traffic from the B1 Road into the neighbourhood of Ondangwa Extension 3 does not align with the demarcated road reserve on the layout plan for Ondangwa Extension 3, which ought to run between Erf 1236, Ondangwa Extension 3, and Erven 6652 and 6653, Ondangwa Extension 28.

With this nature, the proposed development aims to address an encroachment issue in the subject areas of Ondangwa Extension 3 and Ondangwa Extension 28 through a comprehensive approach that includes subdivisions, rezonings, permanent closures, street creation, consolidations of various Erven in Ondangwa Extension 3 and 28, in the Ondangwa Town Planning Scheme, and the alteration of the boundary of Ondangwa Extension 3.

The following town planning steps are required to facilitate the intended development:

### **2.3.1 The Planning Process for Part A, Ondangwa Extension 28**


- **Subdivision of Erf 6651, Ondangwa Extension 28 into Erven A, B & Remainder;**
- **Subdivision of Erf 6652, Ondangwa Extension 28 into Erven A, B & Remainder;**
- **Subdivision of Erf 6653, Ondangwa Extension 28 into Erven A, B & Remainder;**
- **Subdivision of Erf 6654, Ondangwa Extension 28 into Erven A & Remainder;**
- **Consolidation of Erven RE/6651, RE/6652, RE/6653 & RE/6654, Ondangwa Extension 28 into Consolidated Erf Y;**
- **Rezoning of Consolidated Erf Y, Ondangwa Extension 28 from “Business” to “Street”;**
- **Consolidation of Erven B/6651, B6652 & B6653, Ondangwa Extension 28 into Consolidated Erf W;**



- Rezoning of Consolidated Erf W, Ondangwa Extension 28 from “Business” to “Civic”;
- Consolidation of Erven A/6651, A/6652 & A/663 Ondangwa Extension 28 into Consolidated Erf V;
- Rezoning of Consolidated Erf V from “Business” to “Civic”;
- Alternation of Boundaries of Ondangwa Extension 3 to include Consolidated Erf V;
- Inclusion of the rezonings in the next Zoning Scheme to be prepared for Ondangwa.

**a) Subdivision of Erf 6651, Ondangwa Extension 28**


Erf 6651, Ondangwa Extension 28 is to be subdivided into Erven A, B and Remainder as depicted in **Figure 2-5** below. This is to ensure that the road on the layout plan aligns with the exiting road on the ground. Erf A/6651 Ondangwa Extension 28 is currently zoned for Business is proposed to be zoned for civic with the are measuring **6m<sup>2</sup>**, Erf B/6651 Ondangwa Extension 28 is zoned for Business and proposed to be zoned for Business with area measuring **500m<sup>2</sup>** while the Remainder of 6651 Ondangwa Extension 28 is zoned for Business and proposed to be zoned for Street measuring **276m<sup>2</sup>**.

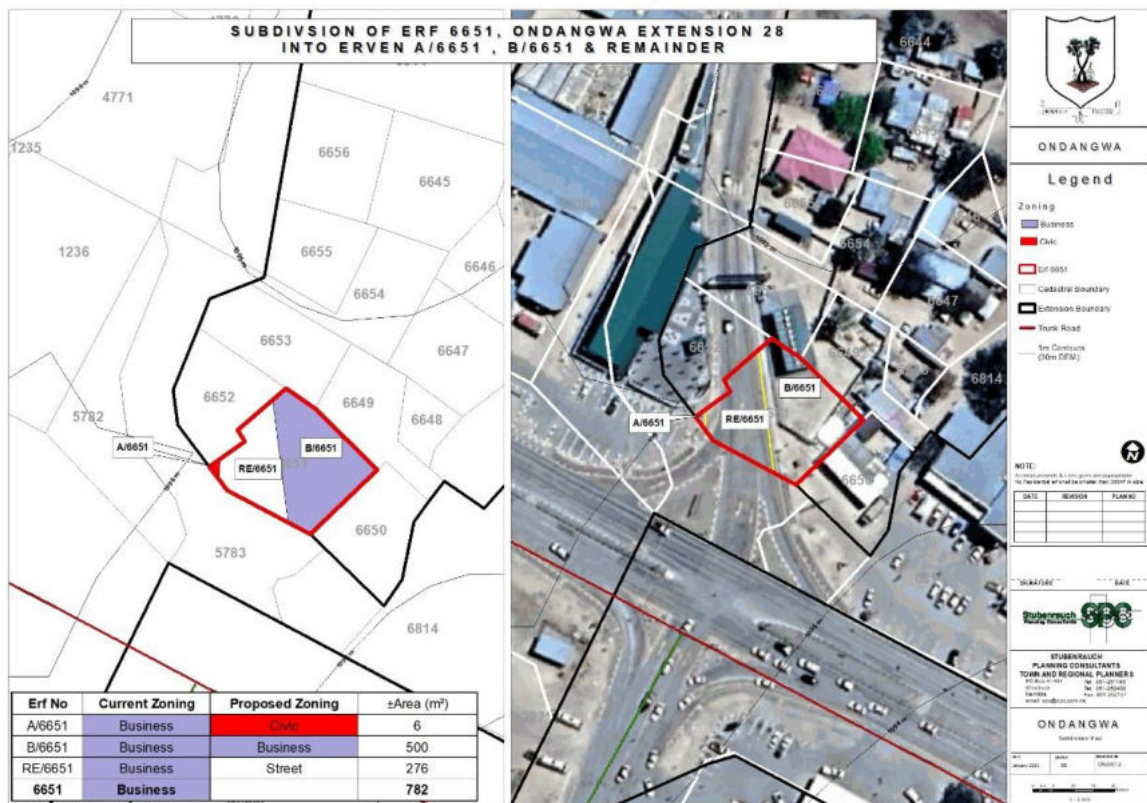

**Figure 2-5:** Subdivision of Erf 6651, Ondangwa Extension 28 into Erven A/6651, B/6651 and Remainder

**b) Subdivision of Erf 6652, Ondangwa Extension 28**

As that of the description on Erf 6651 above, Erf 6652, Ondangwa Extension 28 is to be subdivided into Erven A, B & Remainder as depicted in **Figure 2-6** below. This is also to ensure that the road on the layout plan aligns with the exiting road on the ground. Erf A/6652 Ondangwa Extension 28 is currently zoned for Business is proposed to be zoned for civic with the are measuring **301m<sup>2</sup>**, Erf B/6652 Ondangwa Extension 28 is zoned for Business and proposed to be zoned for Business with area measuring **11m<sup>2</sup>** while the Remainder of 6652 Ondangwa Extension 28 is zoned for Business and proposed to be zoned for Street measuring **235m<sup>2</sup>**.

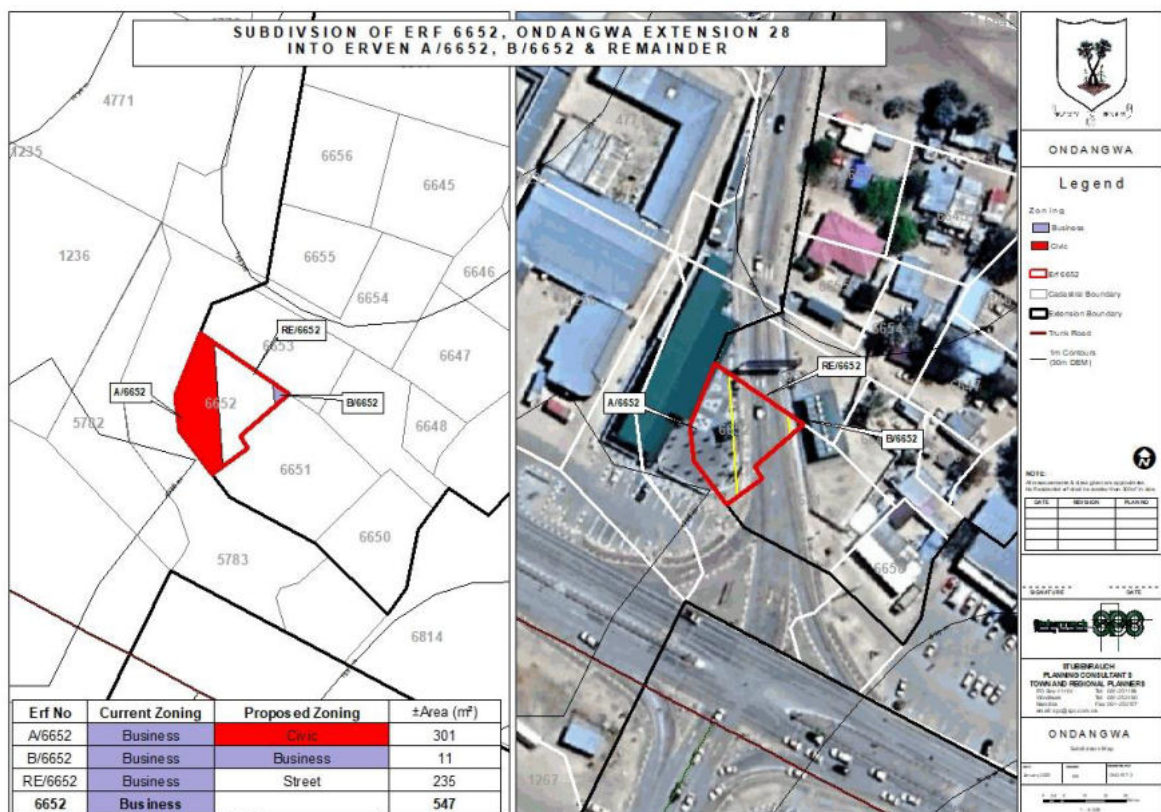


**Figure 2-6:** Subdivision of Erf 6652, Ondangwa Extension 28 into Erven A/6652, B/6652 and Remainder

**c) Subdivision of Erf 6653, Ondangwa Extension 28**

The same as above, Erf 6653, Ondangwa Extension 3 is to be subdivided into Erven A, B & Remainder as depicted in **Figure 2-7** below. This is to ensure that the road on the layout plan aligns with the exiting road on the ground. Erf A/6653 Ondangwa Extension 28 is currently zoned for Business and is proposed to be zoned for civic with the are measuring **24m<sup>2</sup>**, Erf B/6653 Ondangwa Extension 28 is zoned for Business and proposed to be zoned for Business with area measuring **350m<sup>2</sup>** while the Remainder of 6653 Ondangwa Extension 28 is zoned for Business and proposed to be zoned for Street measuring **230m<sup>2</sup>**.




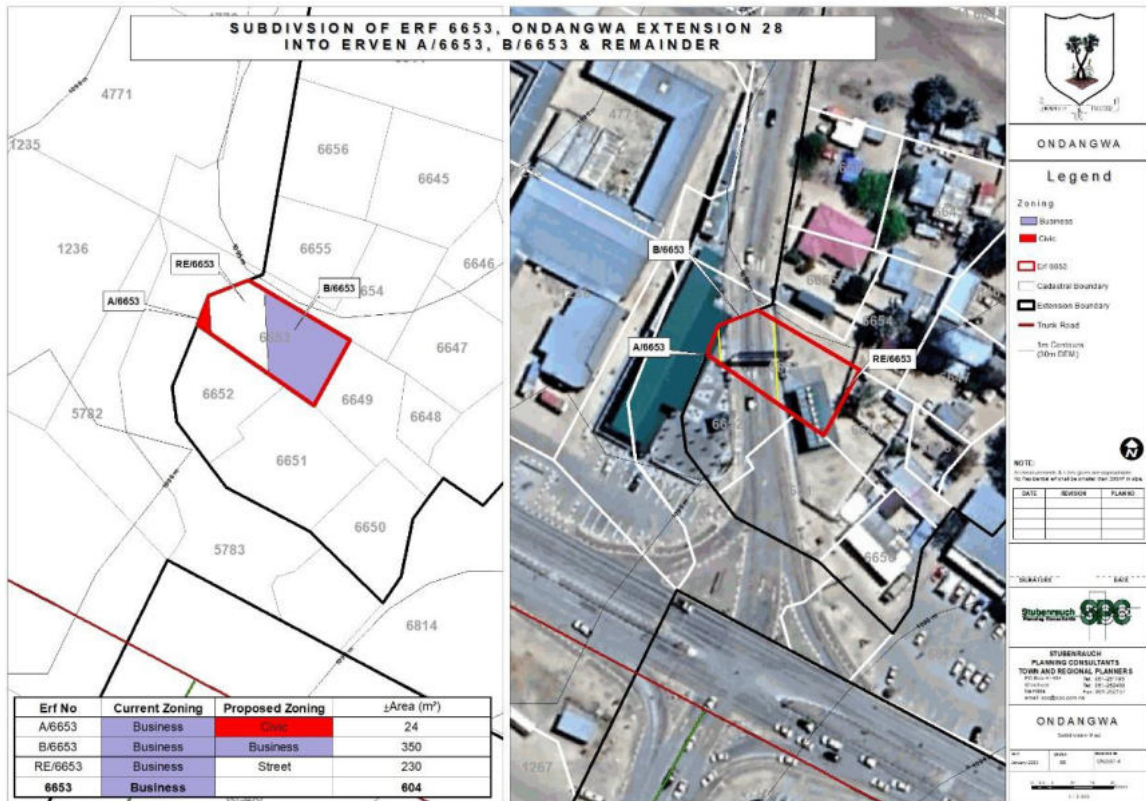

**Figure 2-7:** Subdivision of Erf 6653, Ondangwa Extension 28 into Erven A/6653, B/6653 and Remainder

**d) Subdivision of Erf 6654, Ondangwa Extension 28**


Erf 6654, Ondangwa Extension 3 is to be subdivided into Erf A & Remainder as depicted in **Figure 2-8** below. Erf A/6654 Ondangwa Extension 28 is currently zoned for Business and is to remain zoned for Business with the area measuring **603m<sup>2</sup>**, while the Remainder of 6654 Ondangwa Extension 28 is zoned for Business and proposed to be zoned for Street measuring **8m<sup>2</sup>**.

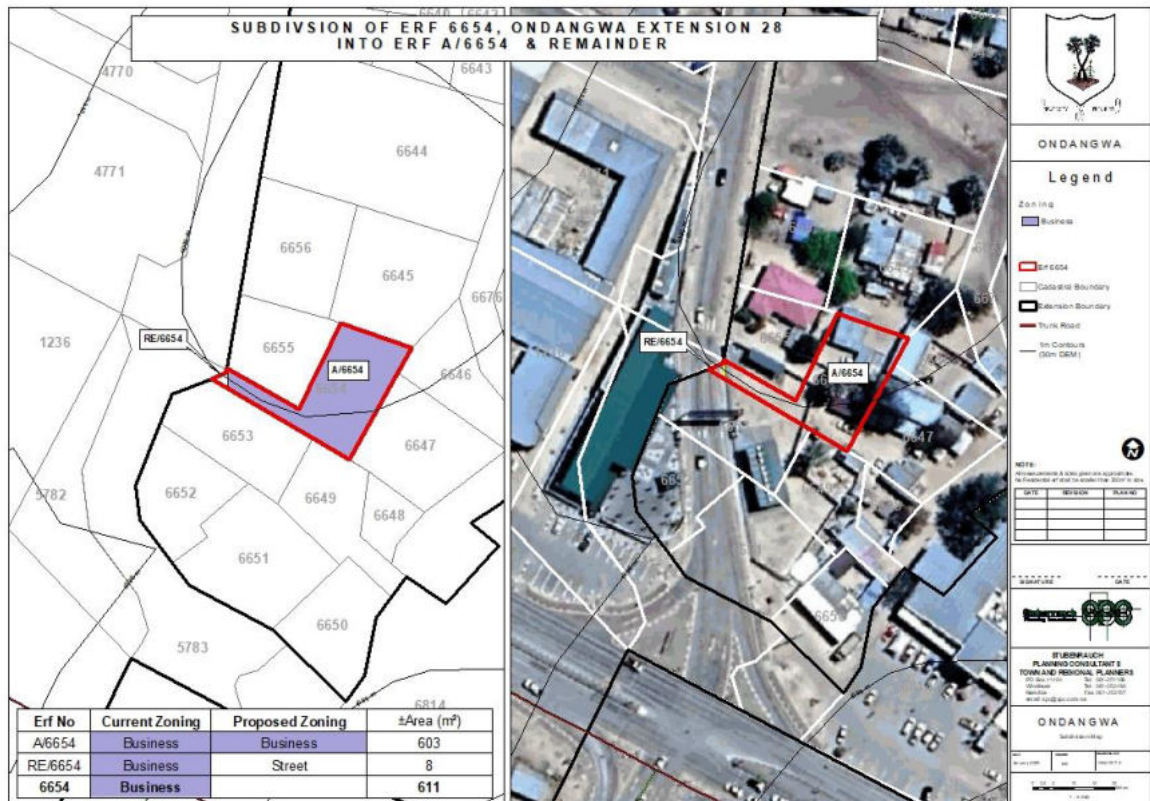

**Figure 2-8:** Subdivision of Erf 6654, Ondangwa Extension 28 into Erven A/6654, and Remainder

**e) Consolidation into Consolidated Erf Y and subsequent rezoning**

The newly created Erven RE/6651, RE/6652, RE/6653 & RE/6654, Ondangwa Extension 28 are to be consolidated into Consolidated Erf Y as depicted in **Figure 2-9** below and subsequently be rezoned from “Business” to “Street” in terms of the Ondangwa Zoning Scheme. This is to ensure that the road on the layout plan aligns with the exiting road on the ground. The Remainder of 6651 Ondangwa Extension 28 is currently zoned for Business and is proposed to be zoned for street with the area measuring **276m²**, the Remainder of 6652 Ondangwa Extension 28 is zoned for Business and proposed to be zoned for Street measuring **235m²**, the Remainder of 6653 Ondangwa Extension 28 is currently zoned for Business and is proposed to be zoned for Street measuring **230m²**, while the Remainder of 6654 Ondangwa Extension 28 is also zoned for Business and is proposed to be zoned for Street measuring **8m²**.

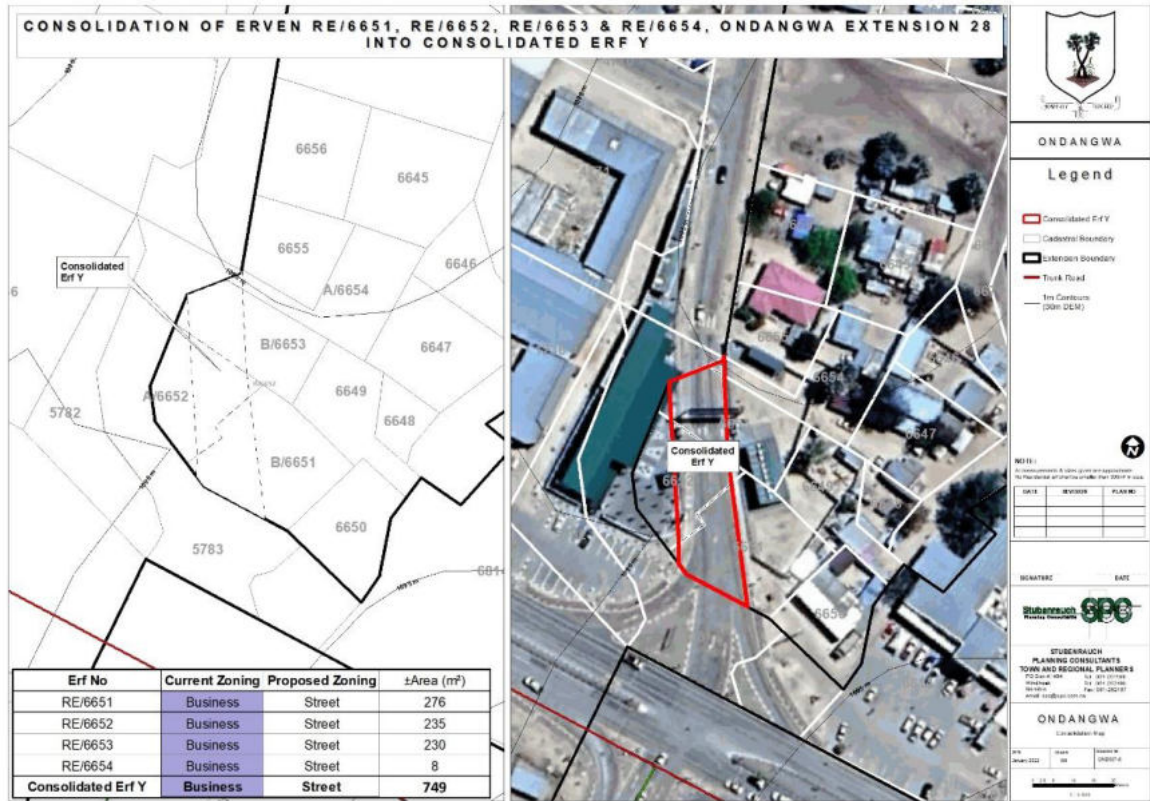


**Figure 2-9:** Consolidation of erven RE/6651, RE/6652, RE/6653 and RE/6654 into Erf Y

**f) Rezoning of Consolidated Erf Y, Ondangwa Extension 28 from “Business” to “Street”**

The Consolidated Erf Y, Ondangwa Extension 28 is to be rezoned from “Business” to “Street” as depicted in **Figure 2-10** below.



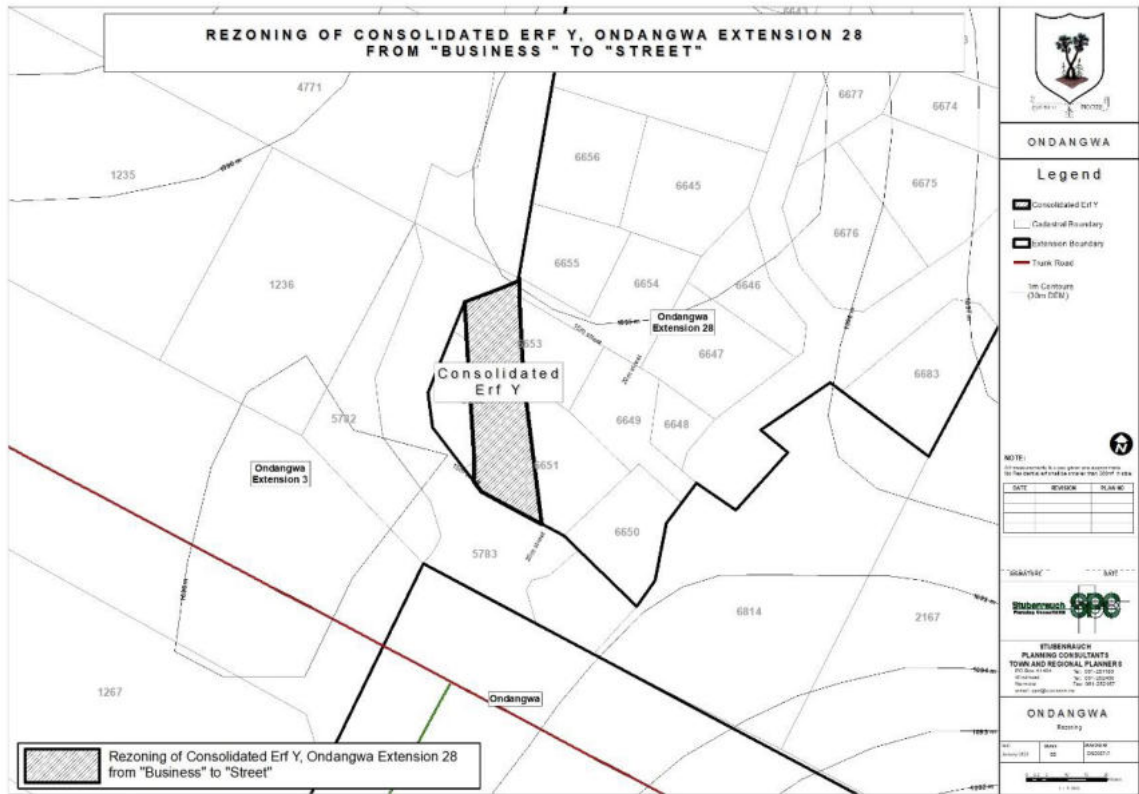

**Figure 2-10:** Rezoning of Consolidated Erf Y, Ondangwa Extension 28 from Business to Street

**g) Consolidation of Erven B/6651, B/6652, B/6653 Ondangwa Extension 28 into Consolidated Erf W**

The newly created Erven B/6651, B6652 & B6653, Ondangwa Extension 28 are to be consolidated into Consolidated Erf W, as depicted in **Figure 2-11** below.

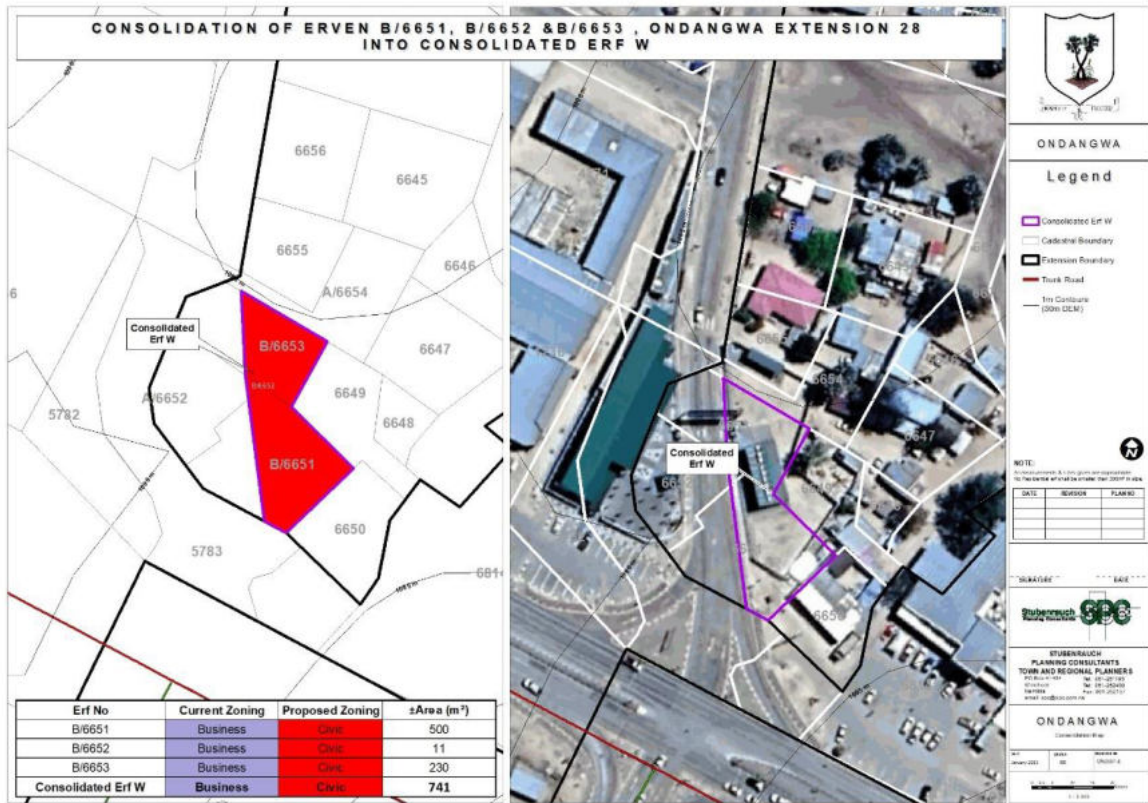


Figure 2-11: Consolidated Erf W

**h) Rezoning of Consolidated Erf W Ondangwa Extension 28 from “Business to “Civic”**

The Consolidated Erf W, as depicted in Figure 2-12 below, is to be rezoned from “Business” to “Civic” in terms to the Ondangwa Zoning Scheme.




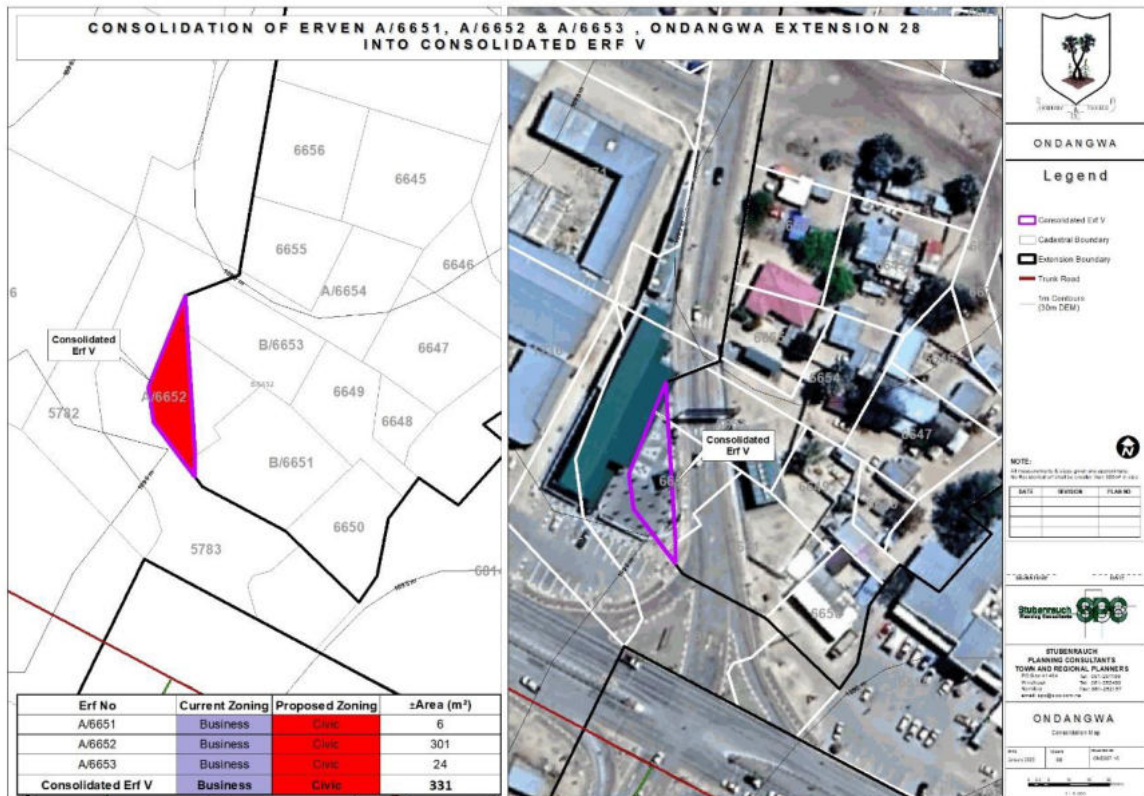


Figure 2-13: Consolidated Erf V, Ondangwa Extension 28

**j) Rezoning of the Consolidated Erf V, Ondangwa Extension 28 from “Business” to “Civic”**

As depicted in Figure 2-14 below, the newly Consolidated Erf V, is to be rezoned from “Business” to “Civic” in terms of the Ondangwa Zoning Scheme. The Consolidated and incorporated Erf V is to be consolidated with Erven B/5782, B/5783, B/Ptn 4, Ondangwa Extension 3 into Consolidated Erf T as depicted in Figure 2-31.



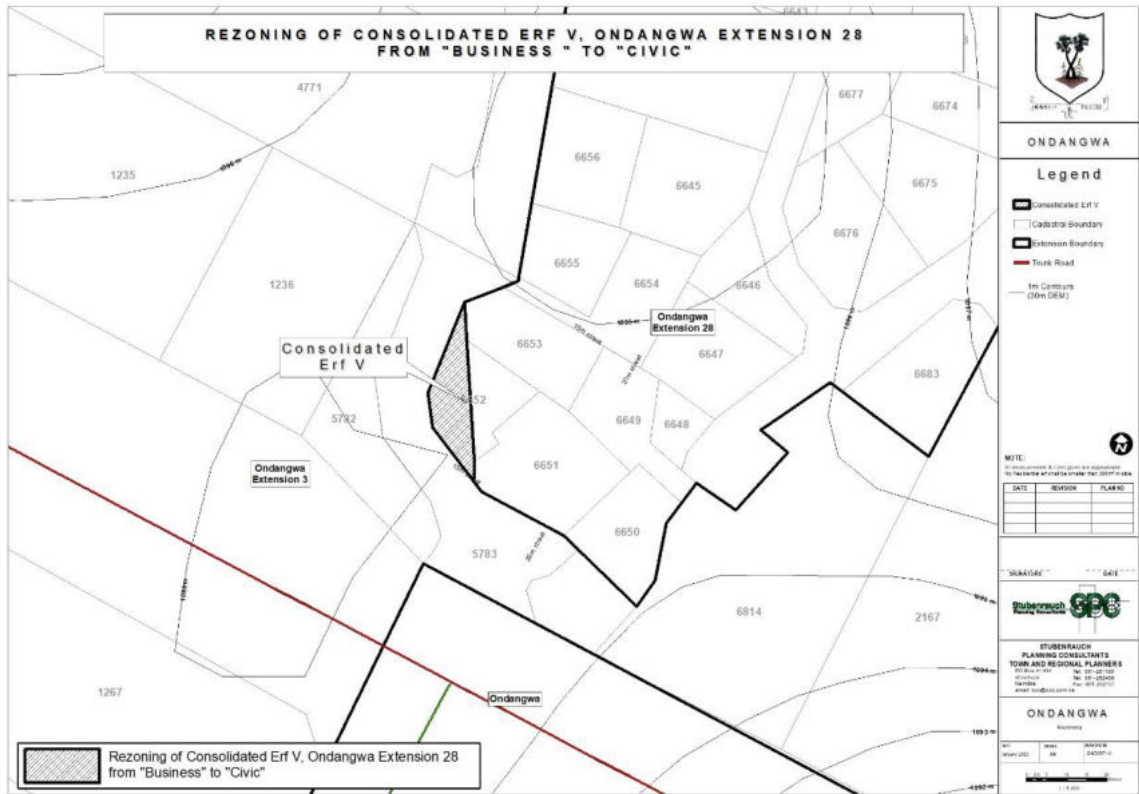

**Figure 2-14:** Rezoned Consolidated Erf V

**k) Alteration of boundaries of Ondangwa Extension 3 to include Consolidated Erf V**

Ondangwa Town Council intends to have the boundaries of the Ondangwa Extension 3 altered as depicted in **Figure 2-15** below, in order to incorporate the Consolidated Erf V which is zoned “Civic” in accordance with the Ondangwa Zoning Scheme.



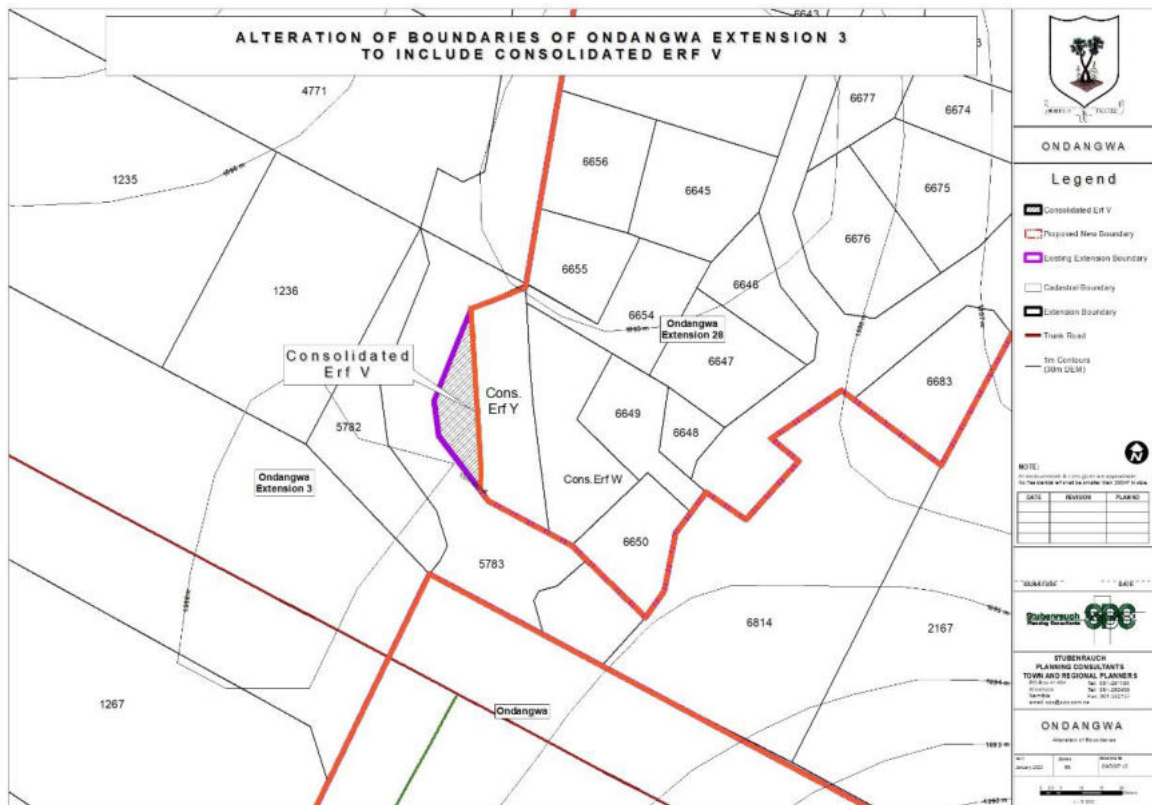


Figure 2-15: Alteration of the boundaries of Ondangwa Extension 3


2.3.2 The Planning Process for Part B, Ondangwa Extension 3

- Subdivision of Erf 4771, Ondangwa Extension 3 into Erven A/4771, B/4771, C/4771 & Remainder;
- Rezoning of Erf B/4771, Ondangwa Extension 3 from “Business” to “Public Open Space”;
- Rezoning of Erf C/4771, Ondangwa Extension 3 from “Business” to “Civic”;
- Consolidation of Erven A/4771 and Erf 1236, Ondangwa Extension 3 into Consolidated Erf Z;
- Consolidation of Erven RE/4771 and Erf 1235, Ondangwa Extension 3 into Consolidated Erf X;
- Subdivision of Erf 5782, Ondangwa Extension 3 into Erven A/5782, B/5782 & Remainder;
- Permanent Closure of Erven B/5782 and RE/5782, Ondangwa Extension 3 as “Public Open Space”;
- Rezoning of Erf B/5782, Ondangwa Extension 3 from “Public Open Space” to “Civic”;
- Rezoning of Erf RE/5782, Ondangwa Extension 3 from “Public Open Space” to “Street”;

- **Subdivision of the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 into Portions A, B & Remainder;**
- **Permanent Closure of Portions A and B of the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 as “Street”;**
- **Rezoning of Portion A/4 of the Farm Ondangwa Town and Townlands No. 882 from “Street” to “Public Open Space”;**
- **Rezoning of Portion B/4 of the Farm Ondangwa Town and Townlands No. 882 from “Street” to “Civic”;**
- **Subdivision of Erf 5783, Ondangwa Extension 3 into Erven A/5783, B/5783, C/5783 and Remainder;**
- **Permanent Closure of Erven A/5783 and B/5783, Ondangwa Extension 3 as “Street”;**
- **Rezoning of Erf A/5783, Ondangwa Extension 3 from “Street” to “Public Open Space”;**
- **Rezoning of Erf B/5783, Ondangwa Extension 3 from “Street” to “Civic”;**
- **Consolidation of Erven A/5782, A/5783, A/Ptn 4 and B/4771, Ondangwa Extension 3 into Consolidated Erf S;**
- **Alternation of Boundaries of Ondangwa Extension 3 to include Consolidated Erf V;**
- **Consolidation of Erven B/5782, B/5783, B/Ptn 4 and Consolidated Erf V, Ondangwa Extension 3 into Consolidated Erf T;**
- **Inclusion of the rezonings in the next Zoning Scheme to be prepared for Ondangwa.**

**A) Subdivision of Erf 4771, Ondangwa Extension 3 into Erven A/4771, B/4771, C/4771 and Remainder**


Erf 4771, Ondangwa Extension 3 is to be subdivided into Erven A/4771, B/4771, C/4771 & Remainder as depicted in **Figure 2-16** below. Erf A/4771 Ondangwa Extension 3 is currently zoned for Business and is to remain zoned for Business with the area measuring **1703m<sup>2</sup>**, while the Remainder of 4771 Ondangwa Extension 3 is zoned for Business and is to remain zoned for Business with area measuring **4783m<sup>2</sup>**.

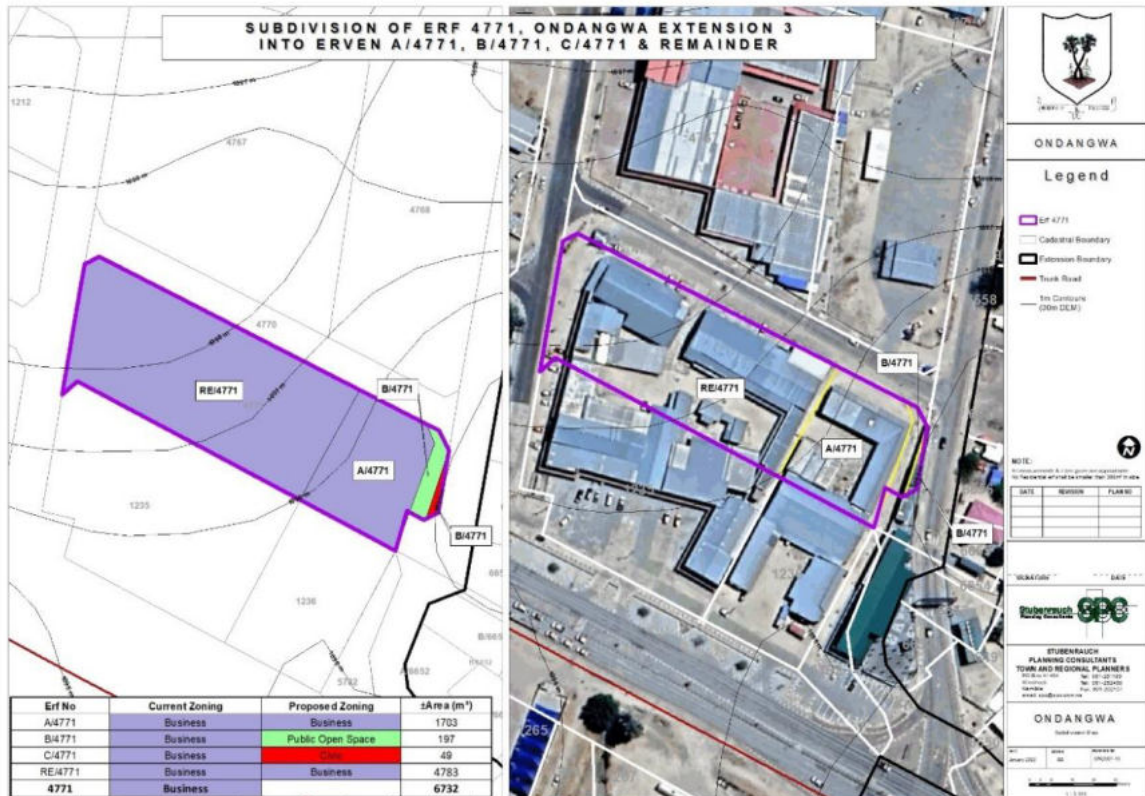

**Figure 2-16:** Subdivision of Erf 4771, Ondangwa Extension 3 into Erven A/4771, B/4771, C/4771 and Remainder.

**B) Rezoning of Erf B/4771 Ondangwa Extension 3 from “Business” to “Public Open Space” and Erf C/4771 Ondangwa Extension 3 from “Business” to “Civic”**

The newly created Erven B/4771 and C/4771, Ondangwa Extension 3 are to be rezoned in terms of the Ondangwa Zoning Scheme respectively from “Business” to “Public Open Space” and from “Business” to “Civic” as depicted in **Figure 2-17** below. Erf B/4771 Ondangwa Extension 3 is zoned for Business and is proposed to be zoned for Public Open Space with area measuring **197m<sup>2</sup>**, Erf C/477 Ondangwa Extension 3 is zoned for Business and is proposed to be zoned for Civic with area measuring **49 m<sup>2</sup>**.

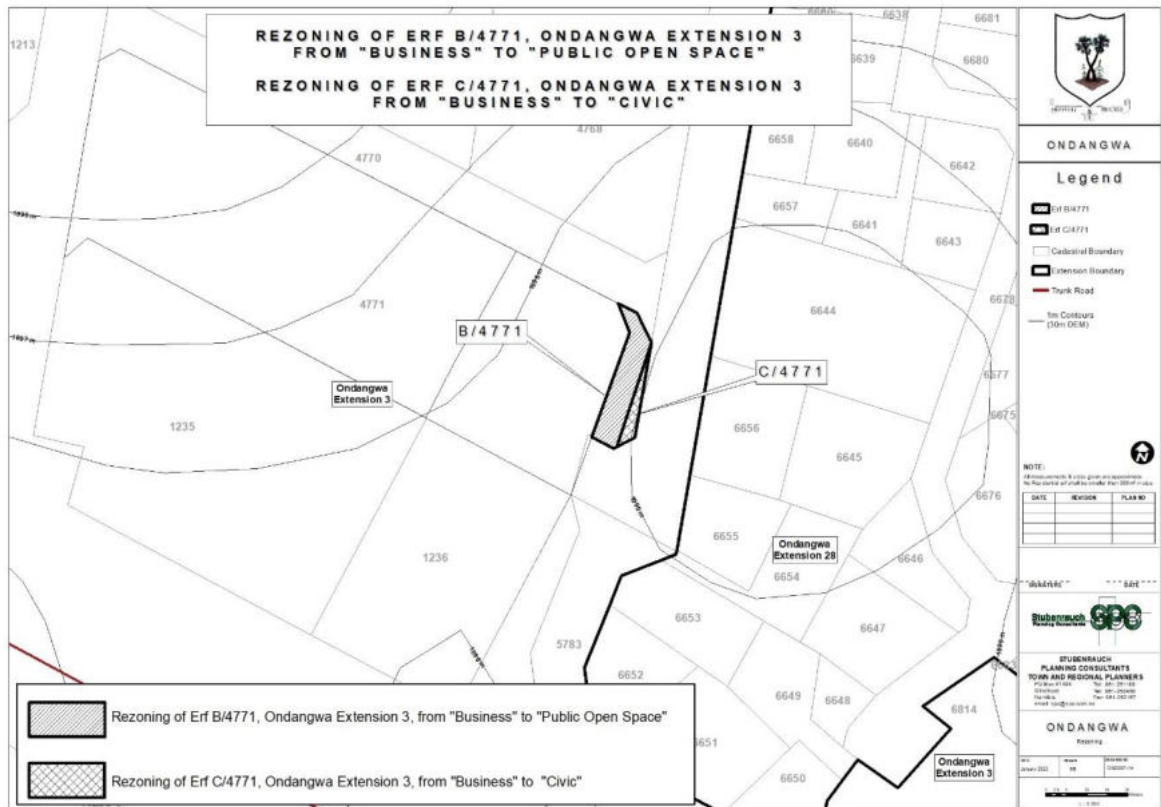


**Figure 2-17:** Rezoning of Erven B/4771 and C/4771 Ondangwa Extension 3

**C) Consolidation of Erf A/4771 and Erf 1236, Ondangwa Extension 3 into Consolidated Erf Z**

The newly created Erf A/4771, Ondangwa Extension 3 is to be consolidated with Erf 1236, Ondangwa Extension 3 into the Consolidated Erf Z as depicted in **Figure 2-18** below. This is to ensure that the buildings for the Huhu City Shopping Complex which have been erected over two properties are accommodated on one erf which will ease the administration duties of the Ondangwa Town Council.



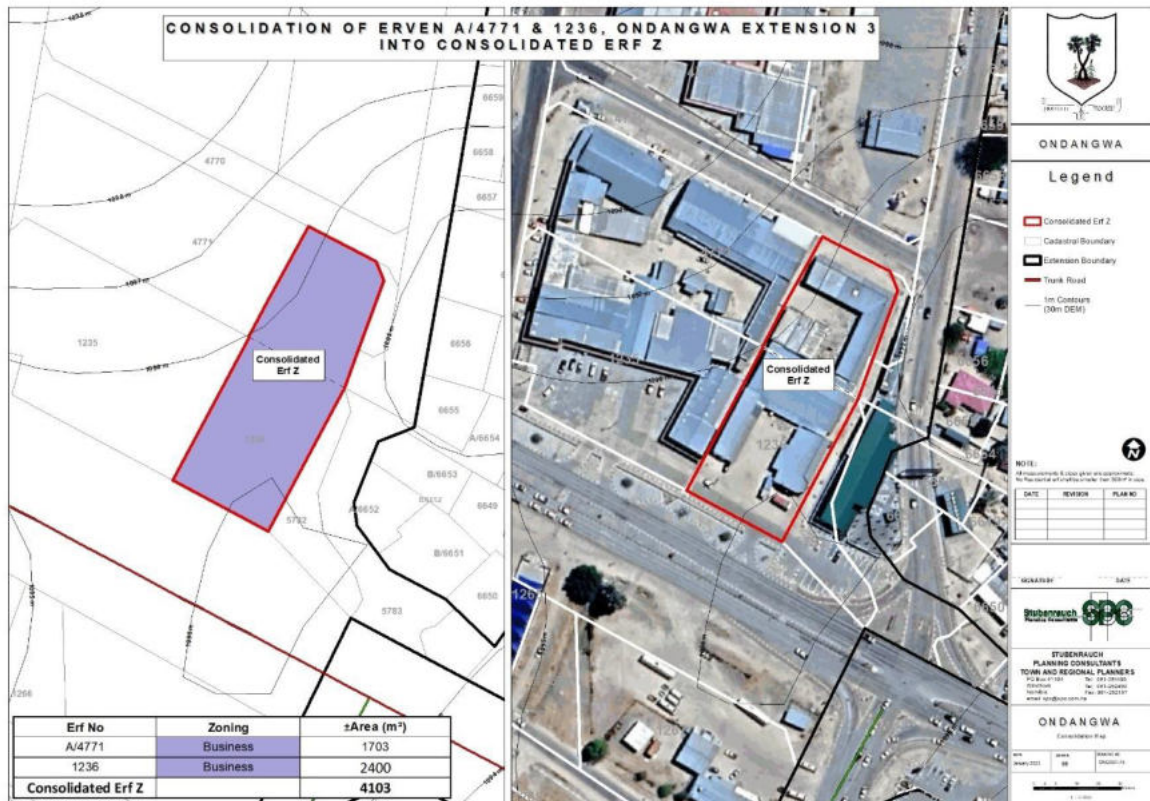

**Figure 2-18: Consolidated Erf Z**

**D) Consolidation Erf RE/4771 and Erf 1235, Ondangwa Extension 3 into Consolidated Erf X**

The Remainder of the subdivided Erf 4771, Ondangwa Extension 3 is to be consolidated with Erf 1235, Ondangwa Extension 3 into the Consolidated **Erf X**, Ondangwa Extension 3 as depicted in **Figure 2-19** below. This is to ensure that the buildings for the Times Square Shopping Centre are accommodated on one erf, easing the administration duties of the Ondangwa Town Council.


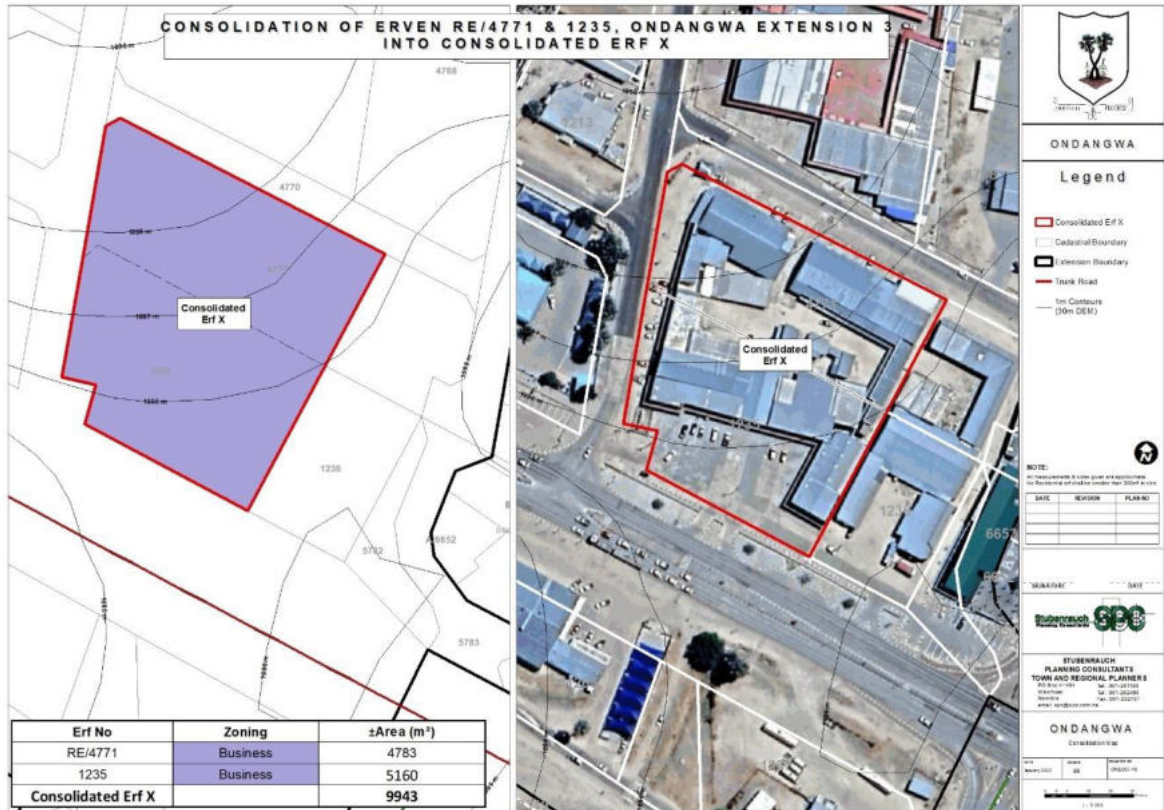


Figure 2-19: Consolidated Erf X

**E) Subdivision of Erf 5782, Ondangwa Extension 3 into Erven A/5784, B/5782 and Remainder**

Erf 5782, Ondangwa Extension 3 is to be subdivided into Erven A/5782, B/5782 & Remainder as depicted in Figure 2-20 below. Erf A/5782, Ondangwa Extension 3 will retain its zoning “Public Open Space”.

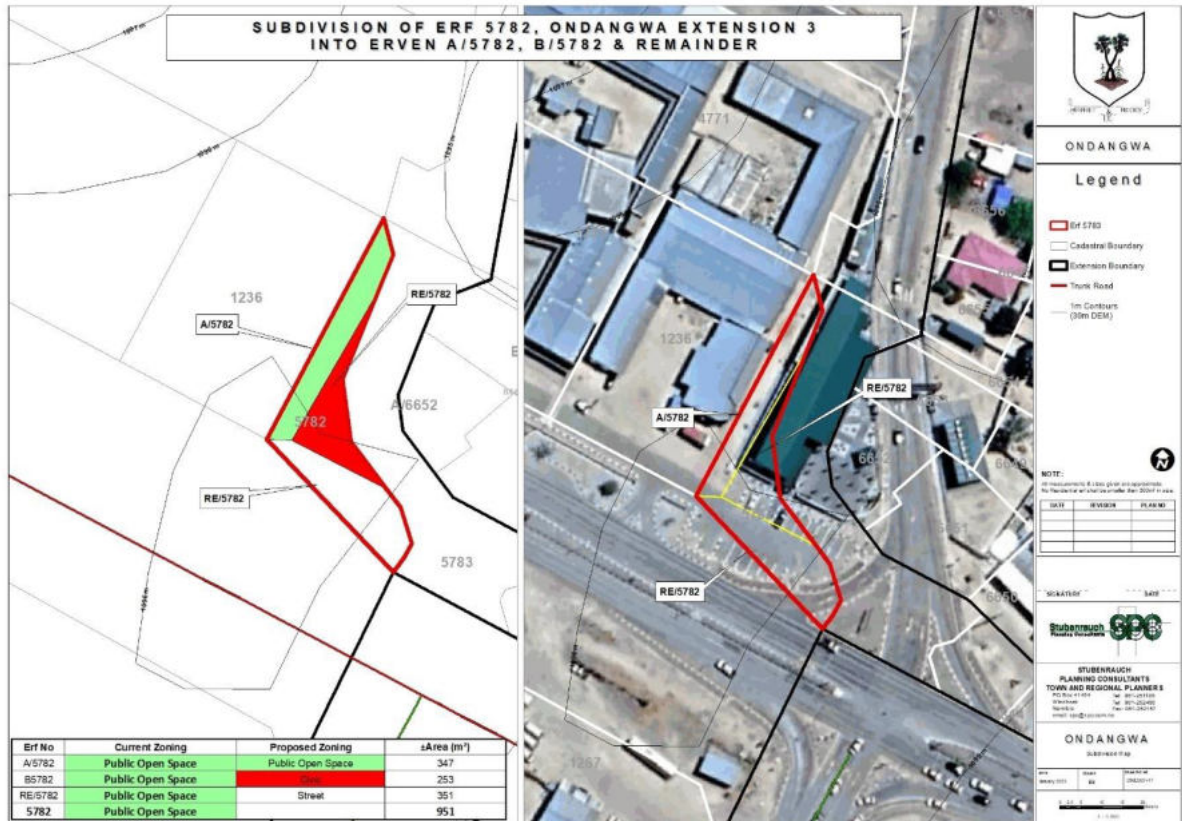

**Figure 2-20:** Subdivision of Erf 5782, Ondangwa Extension 3 into Erven A/5782, B/5782 and Remainder


**F) Permanent Closure of Erven B/5782 and RE/5782, Ondangwa Extension 3 as “Public Open Space”**

The newly created Erven B/5782 and RE/5782, Ondangwa Extension 3 are to be permanently closed as “Public Open Space” as depicted in **Figure 2-21** below.








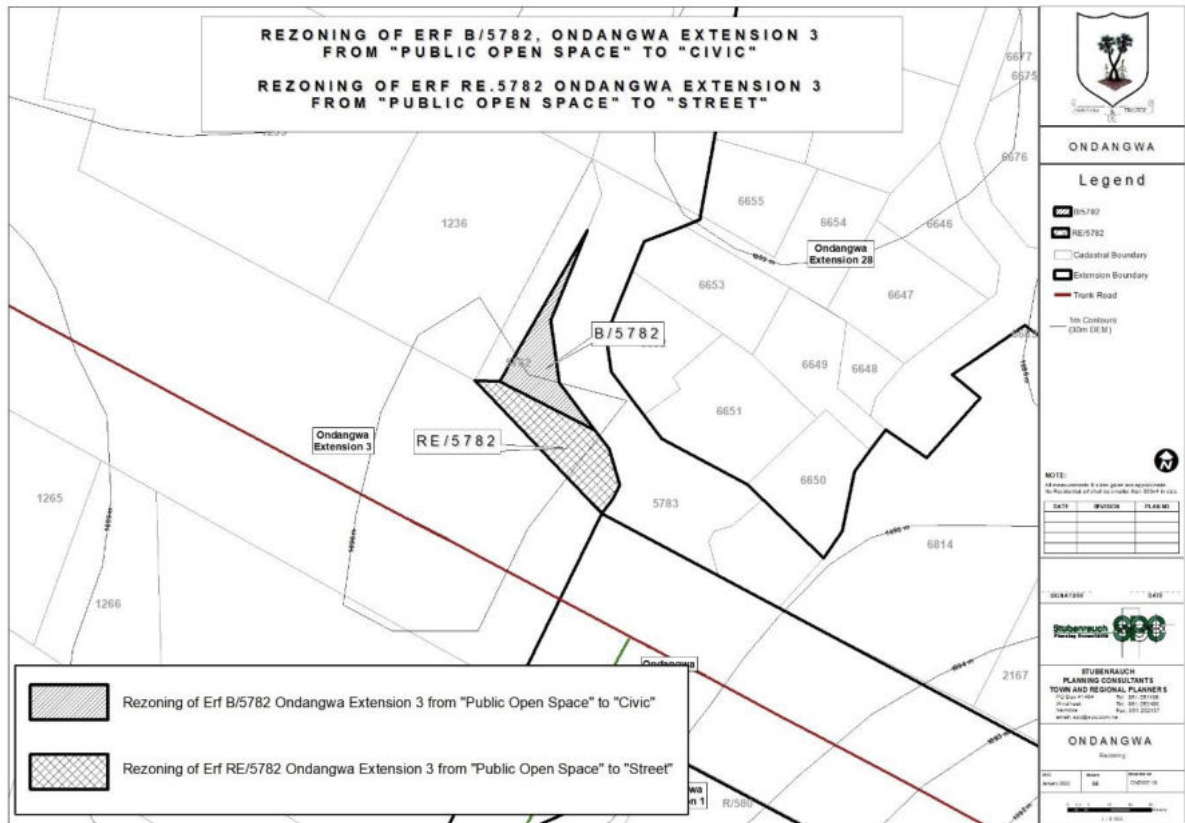

**Figure 2-22:** Rezoning of Erf B/5782 and RE/5782, Ondangwa Extension 3

**H) Subdivision of the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 into Portions A, B and Remainder**


The Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 is to be subdivided into Portion A, B & Remainder as depicted in **Figure 2-23** below.

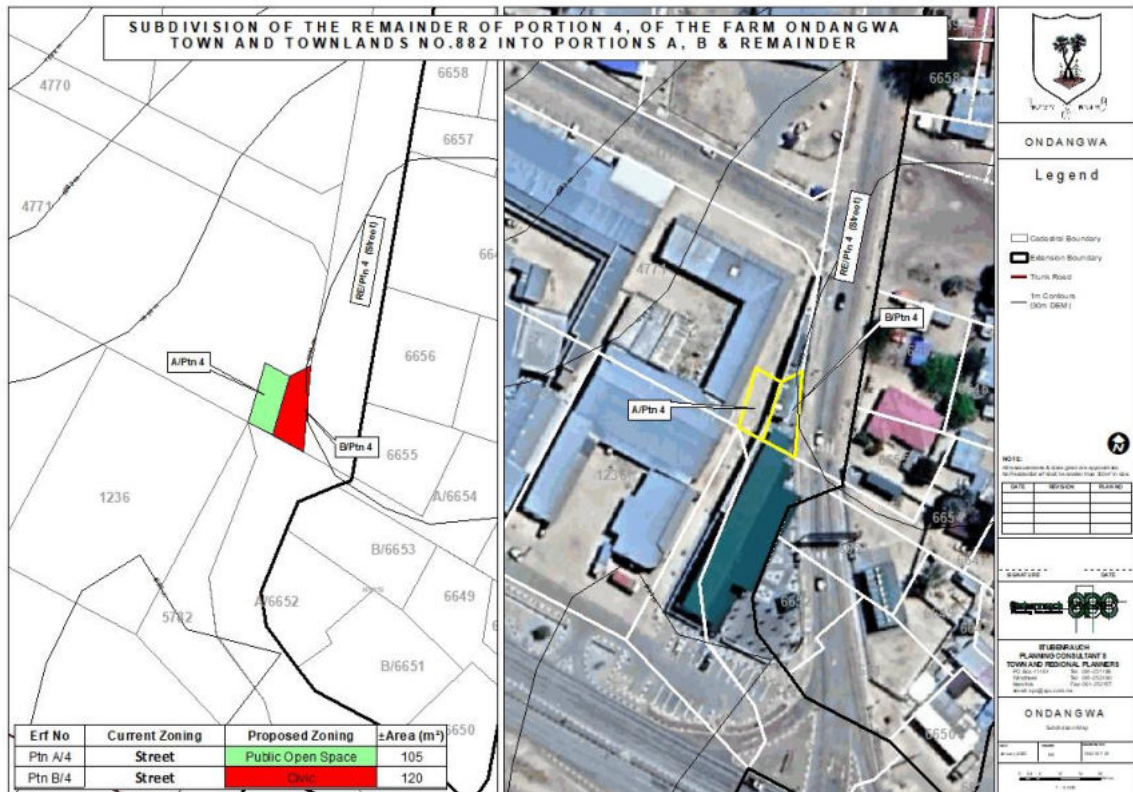

**Figure 2-23:** Subdivision of Portion 4 of the Remainder of the Farm Ondangwa Town and Townlands No. 884

**I) Permanent Closure of Portion A and B of the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 884 as “Street”**

As depicted in **Figure 2-24** below, the newly created Portions A and B of the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 are to be permanently closed as “Street”.

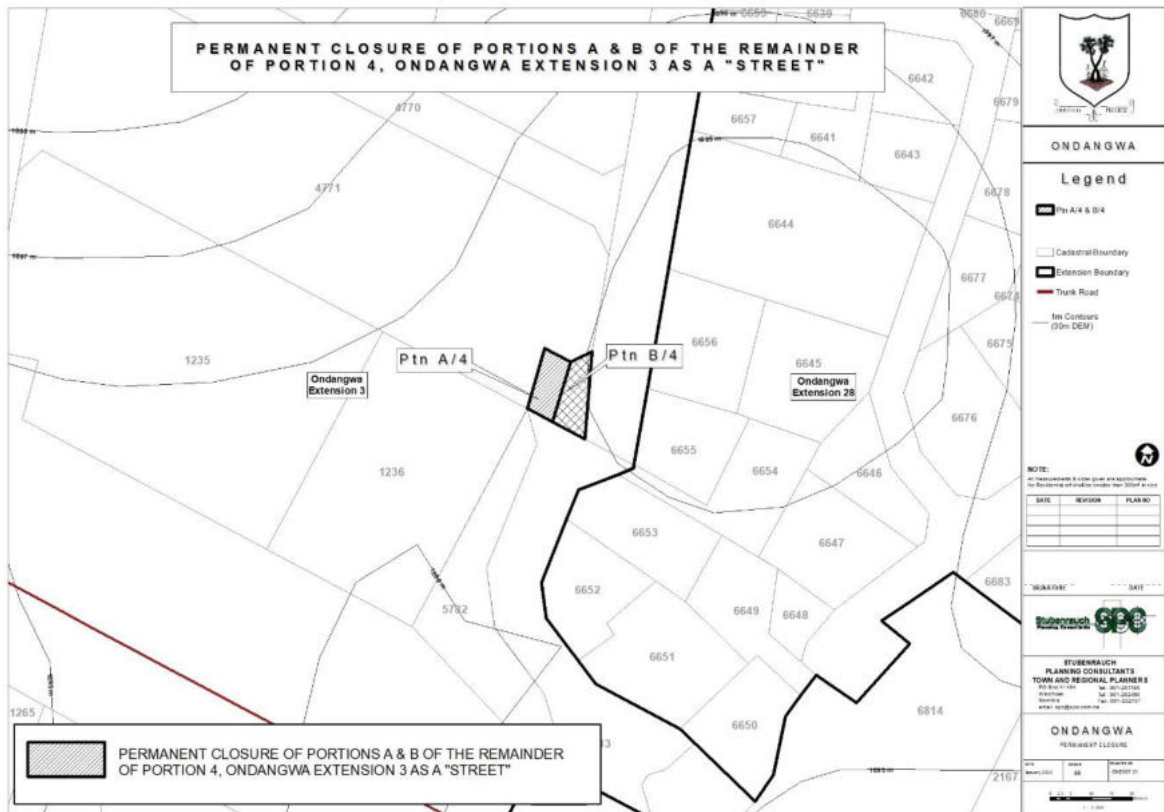

**Figure 2-24:** Permanent Closure of Portion A and B of the Remainder of Portion 4, Ondangwa extension 3 as Street.

**J) Rezoning of Portion A/4 and B/4 the Farm Ondangwa Town and Townland No. 882 from “Street” to “Public Open Space” and to “Civic”**

As depicted in **Figure 2-25** below, the newly created Portions A and B of the Remainder of Portion 4 of the Farm Ondangwa Town and Townlands No. 882 are to be rezoned in terms of the Ondangwa Zoning Scheme respectively from “Street” to “Public Open Space” and “Civic”.






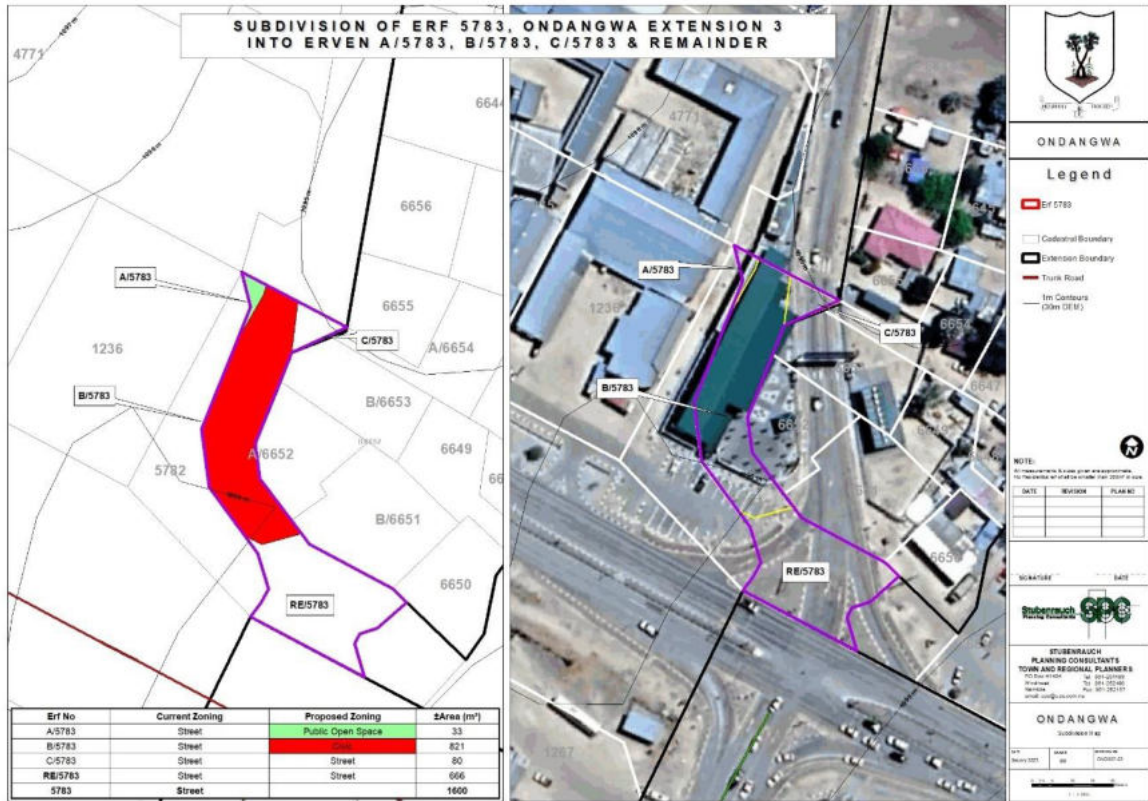


Figure 2-26: Subdivision of Erf 5783 Ondangwa Extension 3

**L) Permanent Closure of Erven A/5783 and B/5783, Ondangwa Extension 3 as “Street”**


As depicted in Figure 2-27 below, the newly created Erven A/5783 and B/5783, Ondangwa Extension 3 are to be permanently closed as “Street”.

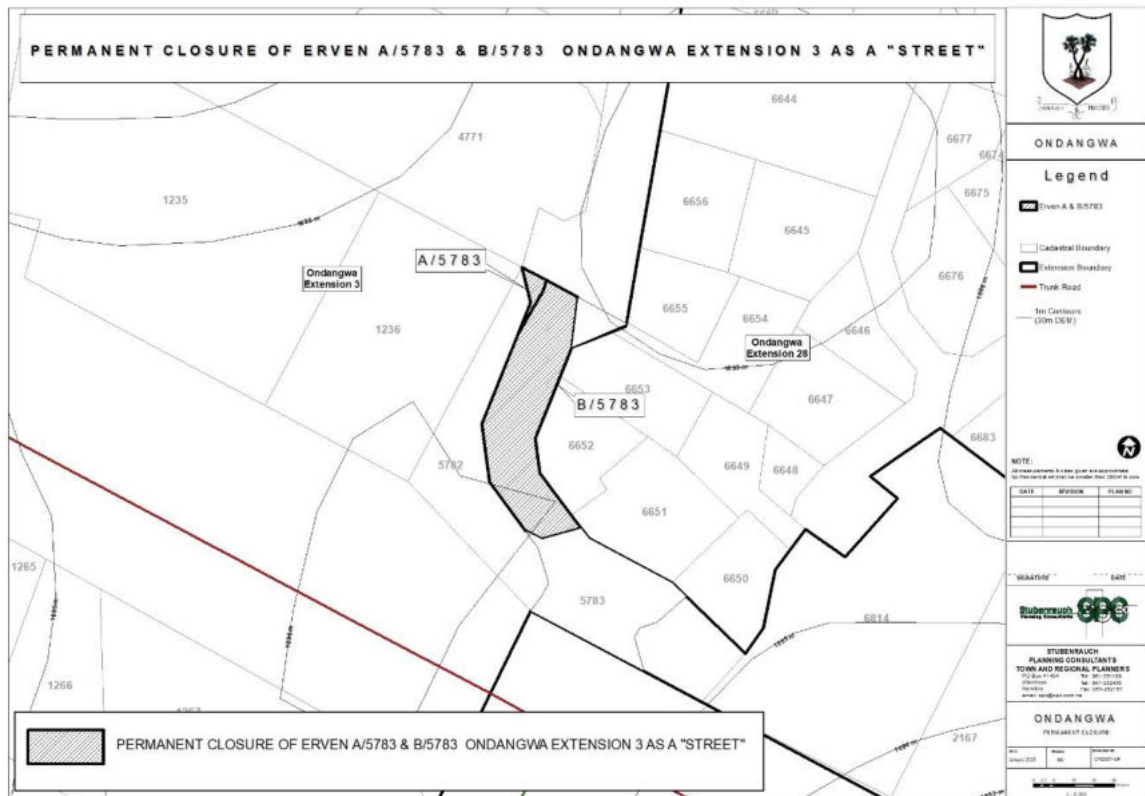

**Figure 2-27:** Permanent Closure of Erven A/5783 and B/5783, Ondangwa Extension 3 as a “Street”

**M) Rezoning of Erven A/5783 Ondangwa Extension 3 from “Street” to “Public Open Space” and B/5783 Ondangwa Extension 3 from “Street” to “Civic”**

As depicted in **Figure 2-28** below, the newly created Erven A/5783 and B/5783, Ondangwa Extension 3 are to be rezoned in terms of the Ondangwa Zoning Scheme respectively from “Street” to “Public Open Space” and “Civic”. Erf A/5783 Ondangwa Extension 3 is zoned for Street and is proposed to be zoned for Public Open Space with area measuring **33m<sup>2</sup>**, Erf B/5783 Ondangwa Extension 3 is zoned for Street and is proposed to be zoned for Civic with area measuring **821 m<sup>2</sup>**.

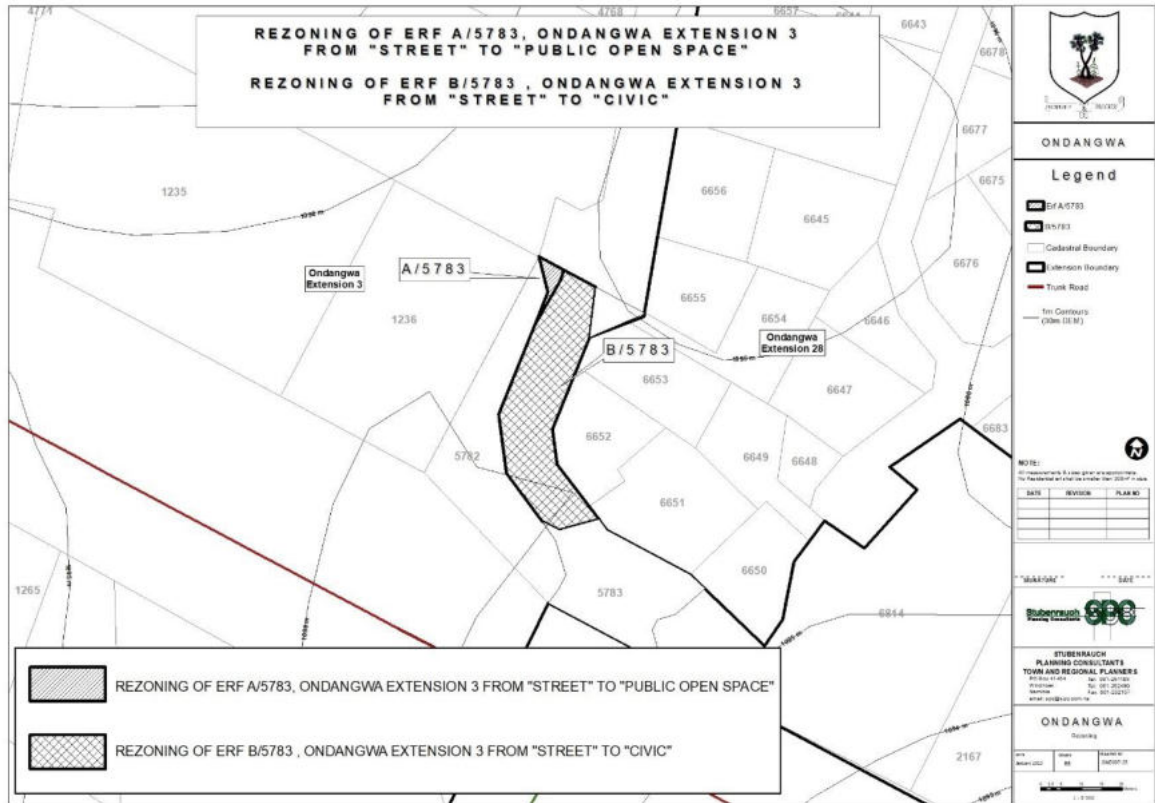

**Figure 2-28:** Rezoning of Erf A/5783 and B/5783, Ondangwa Extension 3

**N) Consolidation Erven A/5782, A/5783, A/Ptn 4 and B/4771, Ondangwa Extension 3 into Consolidated Erf S**

As depicted in **Figure 2-29** below, the newly created Erven A/5782, A/5783, A/Ptn 4 and B/4771, Ondangwa Extension 3, are to be consolidated into the Consolidated Erf S.


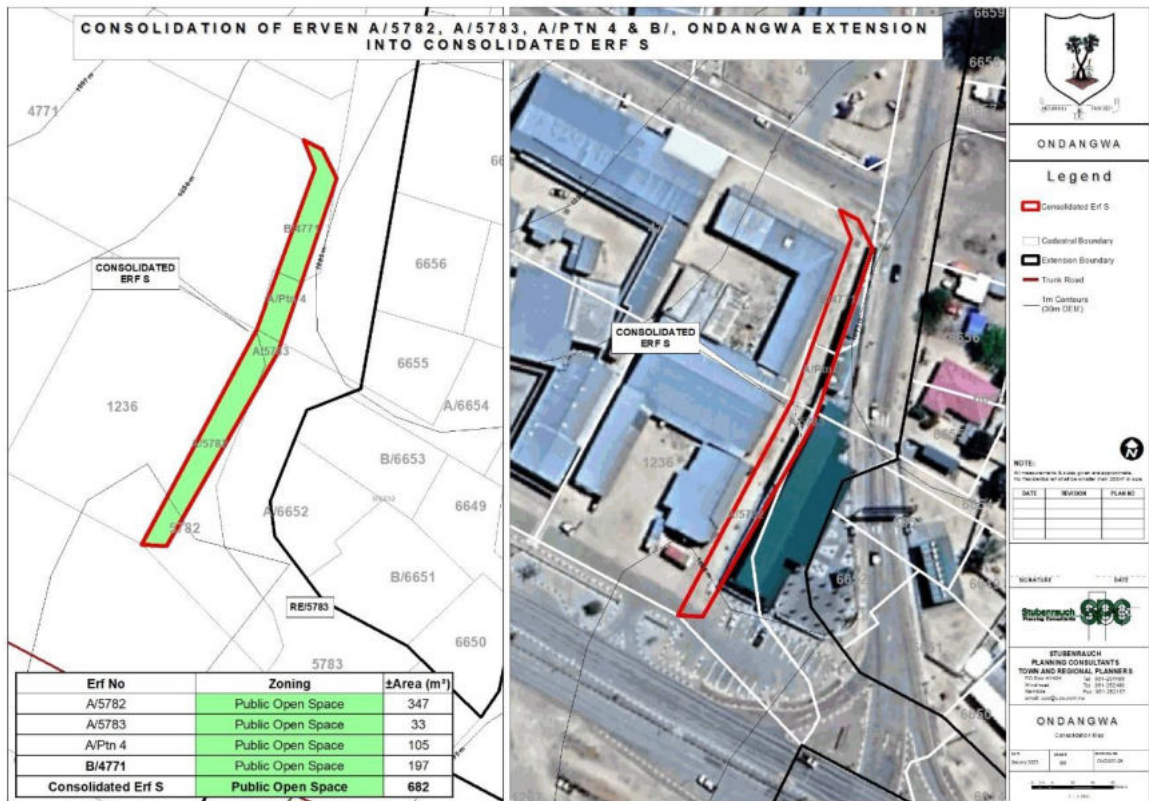


Figure 2-29: Consolidated Erf S

**O) Alteration of boundaries of Ondangwa Extension 3 to include Consolidated Erf V of Extension 28**

As shown earlier in Figure 2-15, it is the same as Figure 2-30 below, the Ondangwa Town Council intends to have the boundaries of the Ondangwa Extension 3 altered, in order to incorporate the Consolidated Erf V of Ondangwa Extension 28, which is zoned “Civic” in accordance with the Ondangwa Zoning Scheme.



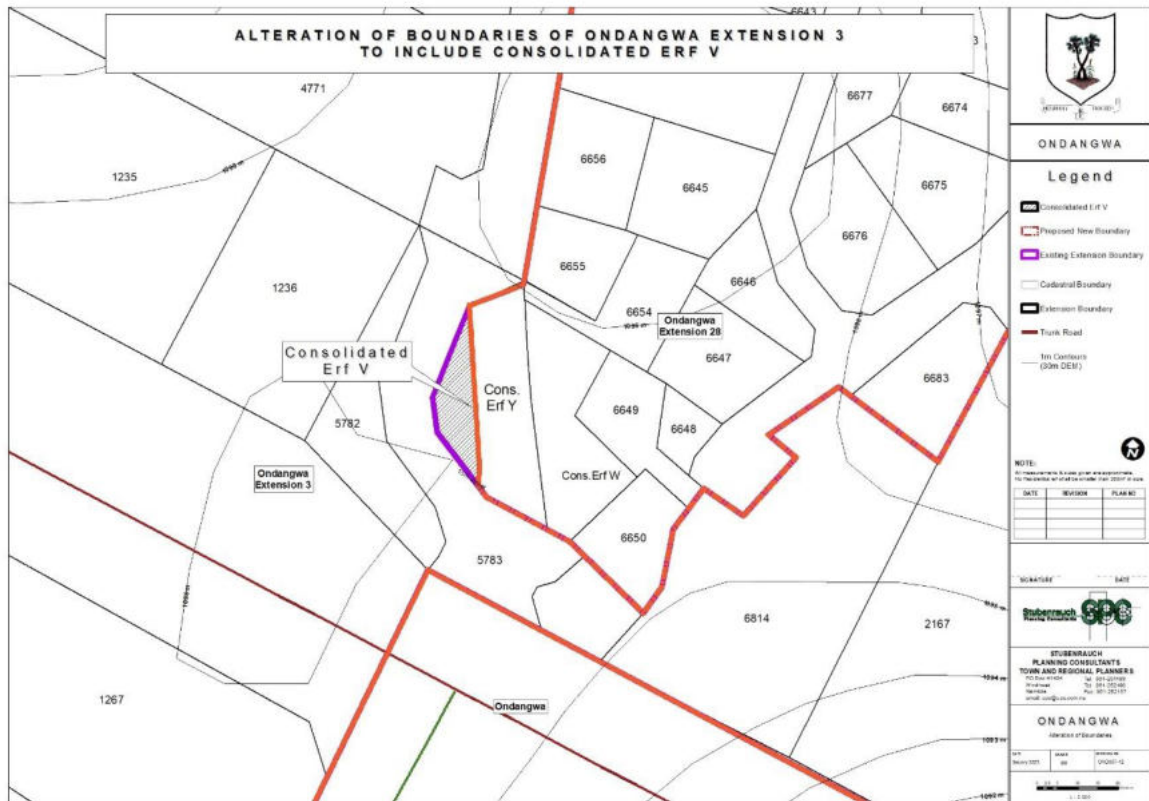

**Figure 2-30:** Alteration of the boundaries of Ondangwa Extension 3 to include Consolidated Erf V

**P) Consolidation of Erven B/5782, B/5783, B/Ptn 4 and the Consolidated Erf V, Ondangwa Extension 3, into Consolidated Erf T**

Erven B/5782, B/5783, B/Ptn 4 and the Consolidated Erf V (*newly incorporated into Ondangwa Extension 3*), Ondangwa Extension 3 are to be Consolidated into the Consolidated Erf T as depicted in **Figure 2-31** below, which accommodates the existing open market (Omatala) in Ondangwa.

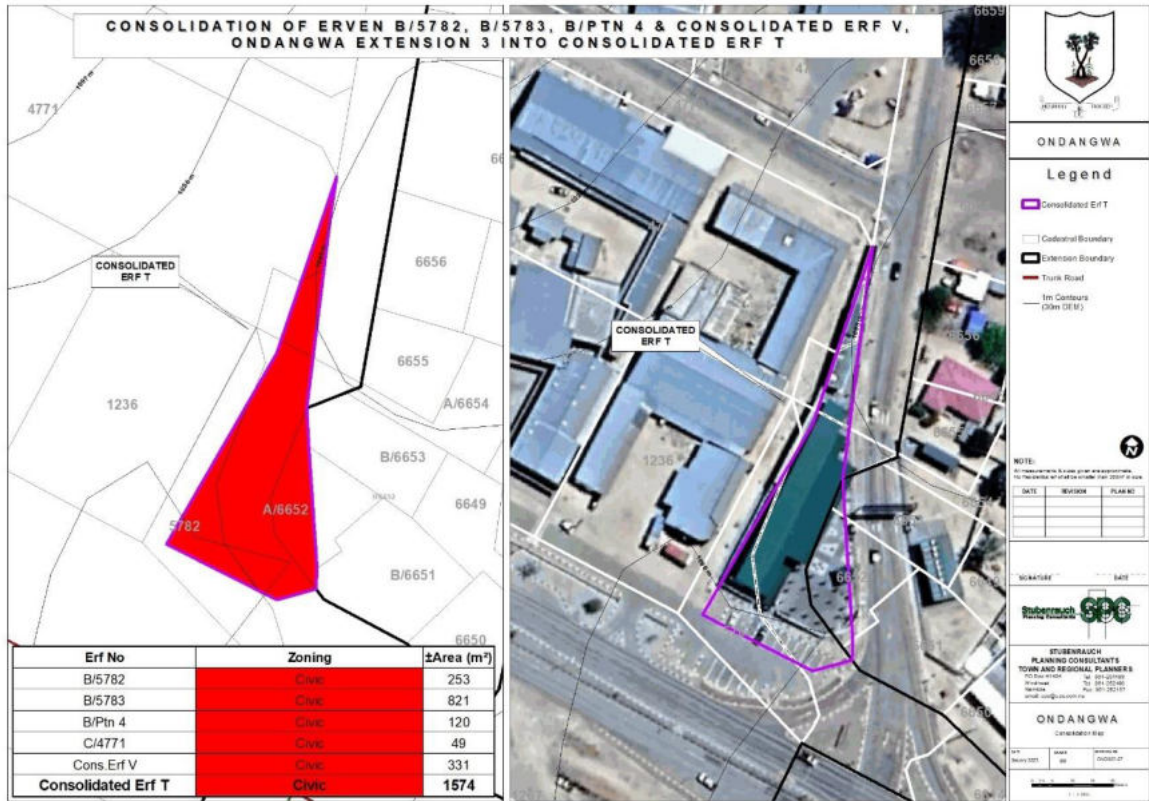


Figure 2-31: Consolidated Erf T

### 3 ROLES AND RESPONSIBILITIES

The proponent (Ondangwa Town Council) is ultimately responsible for the implementation of the EMP, from the planning and design phase to the decommissioning phase (if these developments are in future decommissioned) of these developments. The proponent will delegate this responsibility as the project progresses through its life cycle. The delegated responsibility for the effective implementation of this EMP will rest on the following key individuals:

- Proponent's Representative.
- Environmental Control Officer; and
- Contractor (Construction and Operations and Maintenance).

#### 3.1 COUNCILOR'S REPRESENTATIVE

The Ondangwa Town Council should assign the responsibility of managing all aspects of these developments for all development phases (including all contracts for work outsourced) to a designated member of staff, referred to in this EMP as the Proponent's Representative (CR). The Ondangwa Town Council may decide to assign this role to one person for the full duration of these developments, or may assign a different PR to each of the development phases – i.e. one for the planning and design phase, one for the construction phase and one for the operation and maintenance phase. The CR's responsibilities are as follows:

**Table 3-1** Responsibilities of CR

Responsibility	Project Phase
Making sure that the necessary approvals and permissions laid out in <b>Table 4-1</b> are obtained/adhered to.	<ul style="list-style-type: none"> <li>• Throughout the lifecycle of these developments</li> </ul>
Making sure that the relevant provisions detailed in <b>Table 4-2</b> are addressed during planning and design phase.	<ul style="list-style-type: none"> <li>• Planning and design phase</li> </ul>
Monitoring the implementation of the EMP monthly.	<ul style="list-style-type: none"> <li>• Construction</li> <li>• Operation and maintenance</li> </ul>
Suspending/evicting individuals and/or equipment not complying with the EMP	<ul style="list-style-type: none"> <li>• Construction</li> <li>• Operation and maintenance</li> </ul>
Issuing fines for contravening EMP provisions	<ul style="list-style-type: none"> <li>• Construction</li> </ul>

Responsibility	Project Phase
	<ul style="list-style-type: none"> <li>• Operation and maintenance</li> </ul>

**3.2 ENVIRONMENTAL CONTROL OFFICER**

The CR should assign the responsibility of overseeing the implementation of the whole EMP on the ground during the construction and operation and maintenance phases to an independent external consultant, referred to in this EMP as the Environmental Control Officer (ECO). The CR/ Ondangwa Town Council may decide to assign this role to one person for both phases and may assign a different ECO for each phase. The ECO will have the following responsibilities during the construction and operation and maintenance phases of these developments:

- Management and facilitation of communication between the CR, the contractors, and Interested and Affected Parties (I&APs) with regard to this EMP;
- Conducting site inspections (recommended minimum frequency is weekly) of all construction and/or infrastructure maintenance areas with respect to the implementation of this EMP (audit the implementation of the EMP);
- Assisting the Contractor in finding solutions with respect to matters pertaining to the implementation of this EMP;
- Advising the PR on the removal of person(s) and/or equipment not complying with the provisions of this EMP;
- Making recommendations to the PR with respect to the issuing of fines for contraventions of the EMP; and
- Undertaking an annual review and bi-annual audit of the EMP and recommending additions and/or changes to this document.

**3.3 CONTRACTOR**

Contractors appointed by the Ondangwa Town Council are automatically responsible for implementing all provisions contained within the relevant chapters of this EMP. Contractors will be responsible for the implementation of this EMP applicable to any work outsourced to subcontractors. **Table 4-3** applies to contractors appointed during the construction phase and **Table 4-4** to those appointed during the operation and maintenance phase. To ensure effective environmental management, the afore-mentioned chapters should be included in the applicable contracts for outsourced construction, operation, and maintenance work.

The tables in the following chapter (**Chapter 4**) detail the management measures associated with the roles and responsibilities that have been laid out in this chapter.

## 4 MANAGEMENT ACTIONS

The aim of the management actions in this chapter of the EMP is to avoid potential impacts where possible. Where impacts cannot be avoided, measures are provided to reduce the significance of these impacts.

The following tables provide the management actions recommended to manage the potential impacts rated in the scoping-level EA conducted for these developments. These management actions have been organised temporally according to project phase:

- Applicable legislation (**Table 4-1**);
- Planning and design phase management actions (**Table 4-2**);
- Construction phase management actions (**Table 4-3**);
- Operation and maintenance phase management actions (**Table 4-4**); and
- Decommissioning phase management actions (**Table 4-5**).
- The proponent should assess these **commitments** in detail and should acknowledge their commitment to the specific management actions detailed in the tables below.

### 4.1 ASSUMPTIONS AND LIMITATIONS

This EMP has been drafted with the acknowledgment of the following assumptions and limitations:

- This EMP has been drafted based on the scoping-level Environmental Assessment (EA) conducted for the proposed development. SPC will not be held responsible for the potential consequences that may result from any alterations to the above-mentioned layout.
- It is assumed that construction labourers will be sourced mostly from the Ondangwa Town Council townlands area and that migrant labourers (if applicable) will be housed in established accommodation facilities within Ondangwa.
- No engineering designs have been carried out for the development of the associated services infrastructure (roads, potable water, storm water, sewerage, and electrical reticulations).



#### 4.2 APPLICABLE LEGISLATION

Legal provisions that have relevance to various aspects of these developments are listed in **Table 4-1** below.

**Table 4-1:** Legislation applicable to proposed development

LEGISLATION/POLICIES	RELEVANT PROVISIONS	RELEVANCE TO PROJECT
The Constitution of the Republic of Namibia as Amended	Article 91 (c) provides for duty to guard against “the degradation and destruction of ecosystems and failure to protect the beauty and character of Namibia.”  Article 95(l) deals with the “maintenance of ecosystems, essential ecological processes and biological diversity” and sustainable use of the country’s natural resources.	Sustainable development should be at the forefront of this development.
Environmental Management Act No. 7 of 2007 (EMA)	Section 2 outlines the objective of the Act and the means to achieve that.  Section 3 details the principle of Environmental Management	The development should be informed by the EMA.
EIA Regulations GN 28, 29, and 30 of EMA (2012)	GN 29 Identifies and lists certain activities that cannot be undertaken without an environmental clearance certificate.  GN 30 provides the regulations governing the environmental assessment (EA) process.	The following listed activities are triggered by the proposed development:  <b>Activity 5.1 (d) (Land Use and Development)</b> <b>Activity 10.2 (a) Infrastructure</b> <b>Activity 11 Other Activities</b>
Convention on Biological Diversity (1992)	Article 1 lists the conservation of biological diversity amongst the objectives of the convention.	The project should consider the impact it will have on the biodiversity of the area.
Draft Procedures and Guidelines for conducting EIAs and compiling EMPs (2008)	Part 1, Stage 8 of the guidelines states that if a proposal is likely to affect people, certain guidelines should be considered by the proponent in the scoping process.	The EA process should incorporate the aspects outlined in the guidelines.

LEGISLATION/POLICIES	RELEVANT PROVISIONS	RELEVANCE TO PROJECT
Namibia Vision 2030	Vision 2030 states that the solitude, silence, and natural beauty that many areas in Namibia provide are becoming sought after commodities and must be regarded as valuable natural assets.	Care should be taken that the development does not lead to the degradation of the natural beauty of the area.
Water Act No. 54 of 1956	Section 23(1) deals with the prohibition of pollution of underground and surface water bodies.	The pollution of water resources should be avoided during construction and operation of the development.
The Ministry of Environment, Forestry and Tourism (MEFT) Policy on HIV & AIDS	MEFT has recently developed a policy on HIV and AIDS. In addition, it has also initiated a programme aimed at mainstreaming HIV and gender issues into environmental impact assessments.	The proponent and its contractor must adhere to the guidelines provided to manage the aspects of HIV/AIDS. Experience with construction projects has shown that a significant risk is created when migrant construction workers interact with local communities.
Township and Division of Land Ordinance 11 of 1963	The Townships and Division of Land Ordinance regulates subdivisions of portions of land falling within a Local Authority area	In terms of Section 19 such applications are to be submitted to NAMPAB and Townships Board respectively.
Local Authorities Act No. 23 of 1992	The Local Authorities Act prescribes the manner in which a town or municipality should be managed by the Town or Municipal Council.	The development must comply with provisions of the Local Authorities Act.
Labour Act no. 11 of 2007	Chapter 2 details the fundamental rights and protections. Chapter 3 deals with the basic conditions of employment.	Given the employment opportunities presented by the development, compliance with the labour law is essential.
National Heritage Act No. 27 of 2004	The Act is aimed at protecting, conserving and registering places and objects of heritage significance.	All protected heritage resources (e.g. human remains etc.) discovered, need to be reported immediately to the National Heritage Council (NHC) and require a permit from the NHC before they may be relocated.
Roads Ordinance 17 of 1972	<ul style="list-style-type: none"> <li>Section 3.1 deals with width of proclaimed roads and road reserve boundaries</li> <li>Section 27.1 is concerned with the control of traffic on urban trunk and main roads</li> </ul>	Adhere to all applicable provisions of the Roads Ordinance.

LEGISLATION/POLICIES	RELEVANT PROVISIONS	RELEVANCE TO PROJECT
	<ul style="list-style-type: none"> <li>• Section 36.1 regulates rails, tracks, bridges, wires, cables, subways or culverts across or under proclaimed roads</li> <li>• Section 37.1 deals with Infringements and obstructions on and interference with proclaimed roads.</li> </ul>	
Public and Environmental Health Act of 2015	This Act (GG 5740) provides a framework for a structured uniform public and environmental health system in Namibia. It covers notification, prevention and control of diseases and sexually transmitted infections; maternal, ante-natal and neo-natal care; water and food supplies; infant nutrition; waste management; health nuisances; public and environmental health planning and reporting. It repeals the Public Health Act 36 of 1919 (SA GG 979).	Contractors and users of the proposed development are to comply with these legal requirements.
Nature Conservation Ordinance no. 4 of 1975	Chapter 6 provides for legislation regarding the protection of indigenous plants	Indigenous and protected plants must be managed within the legal confines.
Water Quality Guidelines for Drinking Water and Wastewater Treatment	Details specific quantities in terms of water quality determinants, which wastewater should be treated to before being discharged into the environment	These guidelines are to be applied when dealing with water and waste treatment
Environmental Assessment Policy of Namibia (1995)	The Policy seeks to ensure that the environmental consequences of development projects and policies are considered, understood and incorporated into the planning process, and that the term ENVIRONMENT is broadly interpreted to include biophysical, social, economic, cultural, historical and political components.	This EIA considers this term of Environment.

LEGISLATION/POLICIES	RELEVANT PROVISIONS	RELEVANCE TO PROJECT
Water Resources Management Act No. 11 of 2013	<p>Part 12 deals with the control and protection of groundwater</p> <p>Part 13 deals with water pollution control</p>	<p>The pollution of water resources should be avoided during construction and operation of the development. Should water need to be abstracted, a water abstraction permit will be required from the Ministry of Water, Agriculture and Forestry.</p>
Forest Act 12 of 2001 and Forest Regulations of 2015	<p>To provide for the establishment of a Forestry Council and the appointment of certain officials; to consolidate the laws relating to the management and use of forests and forest produce; to provide for the protection of the environment and the control and management of forest fires; to repeal the Preservation of Bees and Honey Proclamation, 1923 (Proclamation No. 1 of 1923), Preservation of Trees and Forests Ordinance, 1952 (Ordinance No. 37 of 1952) and the Forest Act, 1968 (Act No. 72 of 1968); and to deal with incidental matters.</p>	<p>Protected tree and plant species as per the Forest Act No 12 of 2001 and Forest Regulations of 2015 may not be removed without a permit from the Department of Forestry.</p>
Atmospheric Pollution Prevention Ordinance No 45 of 1965	<p>Part II - control of noxious or offensive gases,</p> <p>Part III - atmospheric pollution by smoke,</p> <p>Part IV - dust control, and</p> <p>Part V - air pollution by fumes emitted by vehicles.</p>	<p>The development should consider the provisions outlined in the act. The proponent should apply for an Air Emissions permit from the Ministry of Health and Social Services (if needed).</p>

LEGISLATION/POLICIES	RELEVANT PROVISIONS	RELEVANCE TO PROJECT
<p>Hazardous Substance Ordinance 14 of 1974</p>	<p>To provide for the control of substances which may cause injury or ill-health to or death of human beings by reason of their toxic, corrosive, irritant, strongly sensitizing or flammable nature or the generation of pressure thereby in certain circumstances; to provide for the division of such substances into groups in relation to the degree of danger; to provide for the prohibition and control of the importation, manufacture, sale, use, operation, application, modification, disposal or dumping of such substances; and to provide for matters connected therewith.</p>	<p>The handling, usage and storage of hazardous substances on site should be carefully controlled according to this Ordinance.</p>
<p>Soil Conservation Act No 76 of 1969</p>	<p>Act to consolidate and amend the law relating to the combating and prevention of soil erosion, the conservation, improvement and manner of use of the soil and vegetation and the protection of the water sources.</p>	<p>The proposed activity should ensure that soil erosion and soil pollution is avoided during construction and operation.</p>



### 4.3 PLANNING AND DESIGN PHASE

The CR should ensure that the management actions detailed below should be adhered to during the period before the construction of the development starts.

**Table 4-2:** Planning and design management actions

Aspect	Management Actions
Visual Impacts	<ul style="list-style-type: none"> <li>• It is recommended that more 'green' technologies be implemented within the architectural designs and building materials of the development where possible to minimise the visual prominence of such a development within the more natural surrounding landscape.</li> <li>• Natural colours and building materials such as wood and stone should be incorporated as well as the use of indigenous vegetation to help beautify the development.               <ul style="list-style-type: none"> <li>○ Visual pollutants can further be prevented through mitigations (i.e. keep existing trees, introduce tall indigenous trees; keep structures unpainted and minimising large advertising billboards).</li> </ul> </li> </ul>
Stormwater	<ul style="list-style-type: none"> <li>• Stormwater runoff should be accommodated within the street creation to ensure that the natural flow of water is not disturbed.</li> </ul>
Existing Service Infrastructure	<ul style="list-style-type: none"> <li>• It is recommended that the subject area should remain connected to the existing services.</li> </ul>
Flora and Fauna (Biodiversity)	<ul style="list-style-type: none"> <li>• Do not clear cut the entire development site, but rather keep the few individual trees/shrubs not directly affecting the developments as part of the landscaping.</li> <li>• Protected trees are not to be removed without a valid permit from the Department of Forestry.</li> </ul>

#### 4.4 CONSTRUCTION PHASE

The management actions listed in **Table 4-3** apply during the construction phase. This table may be used as a guide when developing EMPs for other construction activities within these development areas.

**Table 4-3:** Construction phase management actions

Environmental Feature	Impact	Management Actions	Responsible Person
EMP training	Lack of EMP awareness and the implications thereof.	All construction workers are to undergo EMP training that should include as a minimum the following: <ul style="list-style-type: none"> <li>• Explanation of the importance of complying with the EMP.</li> <li>• Discussion of the potential environmental impacts of construction activities.</li> <li>• Employees’ roles and responsibilities, including emergency preparedness.</li> <li>• Explanation of the mitigation measures that must be implemented when work groups carry out their respective activities.</li> </ul>	Contractor, CR
Conservation of vegetation	Loss of biodiversity	<ul style="list-style-type: none"> <li>• The layout and development design should incorporate existing trees<sup>1</sup>.</li> <li>• The Contractor should compile a Plant Management Plan which should include the following as a minimum:                             <ul style="list-style-type: none"> <li>○ Trees to be preserved should be marked with paint (or other means to be readily visible) and protected.</li> <li>○ Prevent the destruction of protected and endemic plant species. If trees with stem diameter &gt; 20mm be found within the development site, it should be conserved and be made part of the development.</li> </ul> </li> </ul>	Contractor

<sup>1</sup>a “tree” is defined as an indigenous woody perennial plant with a trunk diameter ≥150 mm.

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>○ Trees, which are impossible to conserve, need to be identified and.</li> <li>○ The Contractor should apply to the local authority for a permit to remove these trees (prior to removing them).</li> <li>○ Special protection should be accorded to the protected endemic species, which are to be found within the development area (As per the Forest Act 12 of 2001 and Forest Regulations of 2015).</li> <li>○ Each tree that is removed needs to be replaced with an indigenous tree species after construction.</li> <li>○ Some of these trees can be obtained at the National Botanical Research Institute (NBRI) or at a commercial nursery.</li> <li>● Only a limited width +/- 5 m on the side of roads may be partially cleared of vegetation.</li> <li>● Workers are prohibited from collecting wood or other plant products on or near work sites.</li> <li>● No alien species may be planted on or near work areas.</li> </ul>	
Lay-down areas and materials camp	Loss of biodiversity	<p>Suitable locations for the contractors lay-down areas and materials camp should be identified with the assistance of the PR and the following should be considered in selecting these sites:</p> <ul style="list-style-type: none"> <li>● The areas designated for the services infrastructure should be used as far possible.</li> </ul>	Contractor and PR

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>• Second option should be degraded land.</li> <li>• Avoid sensitive areas (e.g. rivers/drainage lines).</li> </ul>	
Hazardous waste	Contamination of surface and groundwater sources.	<ul style="list-style-type: none"> <li>• All heavy construction vehicles and equipment on site should be provided with a drip tray.</li> <li>• All heavy construction vehicles should be maintained regularly to prevent oil leakages.</li> <li>• Maintenance and washing of construction vehicles should take place only at a designated workshop area and should not take place on open soil.</li> </ul>	Contractor
Water, Sewage, and grey water	Contamination of surface and groundwater sources and water wasting	<ul style="list-style-type: none"> <li>• The wash water (grey water) collected from the cleaning of equipment on-site should not be left standing for long periods of time as this promotes parasite and bacterial proliferation.</li> <li>• Grey water should be recycled:                             <ul style="list-style-type: none"> <li>○ Used for dust suppression.</li> <li>○ Used to water a vegetable garden, or to support a small nursery.</li> <li>○ Used (reused) to clean equipment.</li> </ul> </li> <li>• Grey water that is not recycled should be removed on a regular basis.</li> <li>• No dumping of waste products of any kind in or near water bodies.</li> <li>• Heavy construction vehicles should be kept out of any water bodies and the movement of construction vehicles should be limited where possible to the existing roads and tracks.</li> </ul>	Contractor

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>• Ensure that oil/ fuel spillages from construction vehicles and machinery are minimised and that where these occur, that they are appropriately dealt with.</li> <li>• Drip trays must be placed underneath construction vehicles when not in use to contain all oil that might be leaking from these vehicles.</li> <li>• Contaminated runoff from the construction sites should be prevented from entering the surface and ground water bodies.</li> <li>• All materials on the construction site should be properly stored.</li> <li>• Disposal of waste from the sites should be properly managed and taken to the designated landfill site in Ondangwa.</li> <li>• Construction workers should be given ablution facilities at the construction sites that are located at least 30 m away from any surface water and ground water resources and should be regularly serviced.</li> <li>• Washing of personnel or any equipment should not be allowed on site. Should it be necessary to wash construction equipment these should be done at an area properly suited and prepared to receive and contain polluted waters.</li> </ul>	
General waste	Visual impact and soil contamination	<ul style="list-style-type: none"> <li>• The construction site should be always kept tidy.</li> <li>• All domestic and general construction waste produced daily should be cleaned and contained daily.</li> <li>• No waste may be buried or burned.</li> </ul>	Contractor



Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>• Waste containers (bins) should be emptied regularly and removed from site to a recognised (municipal) waste disposal site.</li> <li>• All recyclable waste needs to be taken to the nearest recycling depot where practical.</li> <li>• Enough separate bins for hazardous and domestic/general waste must be provided on site. These should be clearly marked as such.</li> <li>• Construction labourers should be sensitised to dispose of waste in a responsible manner and not to litter.</li> <li>• No waste may remain on site after the completion of the project.</li> <li>• Strictly, no burning of waste on the site or at the disposal site is allowed as it possess environmental and public health impacts;</li> </ul>	
Topsoil	Loss of topsoil and associated opportunity costs	<ul style="list-style-type: none"> <li>• When excavations are carried out, topsoil<sup>2</sup> should be stockpiled in a demarcated area.</li> <li>• Stockpiled topsoil should be used to rehabilitate post-construction degraded areas and/or other nearby degraded areas if such an area is located a reasonable distance from the stockpile.</li> </ul>	Contractor
Rehabilitation	Visual impact	<ul style="list-style-type: none"> <li>• Upon completion of the construction phase consultations should be held with the local community/property owner(s) regarding the post-construction use of remaining excavated areas (if applicable).</li> </ul>	Contractor, CR

<sup>2</sup> Topsoil is defined here as the top 150mm of surface material, which accounts for the seedbank.

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>• If no post-construction uses are requested, all excavated/degraded areas need to be rehabilitated as follows:                             <ul style="list-style-type: none"> <li>○ Excavated areas may only be backfilled with clean or inert fill. No material of hazardous nature (e.g. sand removed with an oil spill) may be dumped as backfill.</li> <li>○ Rehabilitated excavated areas need to match the contours of the existing landscape.</li> <li>○ The rehabilitated area should not be higher (or lower) than nearby drainage channels. This ensures the efficiency of revegetation and reduces the chances of potential erosion.</li> <li>○ Topsoil is to be spread across excavated areas evenly.</li> <li>○ Deep ripping of areas to be rehabilitated is required, not just simple scarification, to enable rip lines to hold water after heavy rainfall.</li> <li>○ Ripping should be done along slopes, not up and down a slope, which could lead to enhanced erosion.</li> </ul> </li> </ul>	
Road safety	Injury or loss of life	<ul style="list-style-type: none"> <li>• Demarcate roads to be used by construction vehicles clearly.</li> <li>• Off-road driving should not be allowed.</li> <li>• All vehicles that transport materials to and from the site must be roadworthy.</li> </ul>	Contractor

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>• Drivers that transport materials should have a valid driver’s license and should adhere to all traffic rules.</li> <li>• Loads upon vehicles should be properly secured to avoid items falling off the vehicle.</li> </ul>	
Safety around work sites	Injury or loss of life	<ul style="list-style-type: none"> <li>• Excavations should be left open for the shortest time possible.</li> <li>• Excavate short lengths of trenches and box areas for services or foundations in a manner that will not leave the trench unattended for more than 24 hours.</li> <li>• Demarcate excavated areas and topsoil stockpiles with danger tape.</li> <li>• All building materials and equipment are to be stored only within set out and demarcated work areas.</li> <li>• Comply with all waste related management actions stated above in this table.</li> </ul>	Contractor
Ablutions	Non-compliance with Health and Safety Regulations	<ul style="list-style-type: none"> <li>• Separate toilets should be available for men and women and should clearly be indicated as such.</li> <li>• Portable toilets (i.e. easily transportable) should be available at every construction site:                             <ul style="list-style-type: none"> <li>○ 1 toilet for every 15 females.</li> <li>○ 1 toilet for every 30 males.</li> <li>○ Sewage needs to be removed on a regular basis to an approved (municipal) sewage disposal site in Ondangwa.</li> </ul> </li> </ul>	Contractor

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>○ Alternatively, sewage may be pumped into sealable containers and stored until it can be removed.</li> <li>○ Workers responsible for cleaning the toilets should be provided with environmentally friendly detergents, latex gloves, and masks.</li> </ul>	
Open fires	Injury or loss of life	<ul style="list-style-type: none"> <li>● No open fires may be made anywhere on site.</li> </ul>	Contractor
General health and safety	Injury or loss of life	<ul style="list-style-type: none"> <li>● A fully stocked first aid kit should permanently be available on-site as well as an adequately trained member of staff capable of administering first aid.</li> <li>● All workers should have access to the relevant personal protective equipment (PPE).</li> <li>● Sufficient potable water reserves should be always available to workers.</li> <li>● No person should be allowed to smoke close to fuel storage facilities or portable toilets (if toilets are chemical toilets – the chemicals are flammable).</li> <li>● No workers should be allowed to drink alcohol during work hours.</li> <li>● No workers should be allowed on site if under the influence of alcohol.</li> <li>● Building rubble and domestic waste should be stored in skips.</li> <li>● Condoms should be accessible/available to all construction workers.</li> <li>● Access to Antiretroviral medication should be facilitated.</li> </ul>	Contractor



Environmental Feature	Impact	Management Actions	Responsible Person
Dust	Nuisance and health impacts	<ul style="list-style-type: none"> <li>• A watering truck should be used on gravel roads with the heaviest vehicle movement especially during dry and windy conditions. However, due consideration should be given to water restrictions during times of drought.</li> <li>• The use of waterless dust suppression means (e.g. lignosulphonate products such as Dustex) should be considered.</li> <li>• Cover any stockpiles with plastic to minimise windblown dust.</li> <li>• Dust protection masks should be provided to workers if they complain about dust.</li> <li>• Vehicles travelling to and from the construction site must adhere to the speed limits to avoid producing excessive dust. A speed limit of 40 km/hr should be set for all vehicles travelling over exposed areas.</li> </ul>	Contractor
Noise	Nuisance impacts	<p>Work hours should be restricted to between 08h00 and 17h00 and 7:30 – 13:00 on Saturdays where construction involving the use of heavy equipment, power tools and the movement of heavy vehicles is less than 500 m from residential areas. If an exception to this provision is required, all residents within the 500 m radius should be given 1 week’s written notice.</p> <ul style="list-style-type: none"> <li>• Provide ear plugs and earmuffs to staff undertaking the noisy activity or working within proximity thereof or alternatively, all construction workers should be equipped with ear protection equipment.</li> </ul>	Contractor

Environmental Feature	Impact	Management Actions	Responsible Person
Recruitment of labourers	Negative conflict regarding recruitment	<p>The Contractor should adhere to the below provision as a minimum for the recruitment of labour:</p> <ul style="list-style-type: none"> <li>• Adhere to the legal provisions in the Labour Act for the recruitment of labour (target percentages for gender balance, optimal use of local labour and SME's, etc.).</li> <li>• Recruitment should not take place at construction sites.</li> <li>• Ensure that all sub-contractors are aware of recommended recruitment procedures and discourage any recruitment of labour outside these agreed upon procedures.</li> <li>• Contractors should give preference in terms of recruitment of sub-contractors and individual labourers to those who are qualified and from the Ondangwa project area and only then look to surrounding towns.</li> <li>• Clearly explain to all jobseekers the terms and conditions of their respective employment contracts (e.g. period of employment etc.) – make use of interpreters where necessary.</li> </ul>	Contractor
Communication plan	Negative conflict with I&APs	<p>The Contractor or proponent should draft a Communication Plan, which should outline as a minimum the following:</p> <ul style="list-style-type: none"> <li>• How Interested and Affected Parties (I&amp;APs), who require ongoing communication for the duration of the construction period, will be identified and recorded and who will manage and update these records.</li> </ul>	Contractor

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>• How these I&amp;APs will be consulted on an ongoing basis.</li> <li>• Make provision for grievance mechanisms – i.e. how concerns can be lodged/ recorded and how feedback will be delivered as well as further steps of arbitration in the event that feedback is deemed unsatisfactory.</li> </ul>	
General communication	Negative conflict with I&APs	<ul style="list-style-type: none"> <li>• The PR must appoint an ECO to liaise between the Contractor, I&amp;APs, Developer.</li> <li>• The Contractor shall at every monthly site meeting report on the status of the implementation of all provisions of the EMP.</li> <li>• The Contractor should implement the EMP awareness training as stipulated above in this table.</li> <li>• The Contractor must list the I&amp;APs of the project and their contact details with whom ongoing communication would be required for the duration of the contract. This list, together with the Communication Plan must be agreed upon and given to the PR before construction commences.</li> <li>• The Communication Plan, once agreed upon by the Developer, shall be legally binding.</li> <li>• All communication with the I&amp;APs must take place through the ECO.</li> <li>• A copy of the EMP must be available at the site office and should be accessible to all I&amp;APs.</li> </ul>	Contractor, ECO, CR

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>• Key representatives from the above-mentioned list need to be invited to attend monthly site meetings to raise any concerns and issues regarding project progress.</li> <li>• The Contractor should liaise with the Developer regarding all issues related to community consultation and negotiation before construction commences.</li> <li>• A procedure should be put in place to ensure that concerns raised have been followed-up and addressed.</li> <li>• All people on the I&amp;APs list should be informed about the availability of the complaints register and associated grievance mechanisms in writing by the PR prior to the commencement of construction activities.</li> </ul>	
Archaeology	Loss of heritage resources	<ul style="list-style-type: none"> <li>• Should a heritage site or archaeological site be uncovered or discovered during the construction phase of the project, a “chance find” procedure should be applied in the order they appear below:                             <ul style="list-style-type: none"> <li>○ If operating machinery or equipment, stop work;</li> <li>○ Demarcate the site with danger tape;</li> <li>○ Determine GPS position if possible;</li> <li>○ Report findings to the construction foreman;</li> <li>○ Report findings, site location and actions taken to superintendent;</li> <li>○ Cease any works in immediate vicinity;</li> </ul> </li> </ul>	Contractor

Environmental Feature	Impact	Management Actions	Responsible Person
		<ul style="list-style-type: none"> <li>○ Visit site and determine whether work can proceed without damage to findings;</li> <li>○ Determine and demarcate exclusion boundary;</li> <li>○ Site location and details to be added to the project’s Geographic Information System (GIS) for field confirmation by archaeologist;</li> <li>○ Inspect site and confirm addition to project GIS;</li> <li>○ Advise the National Heritage Council of Namibia (NHCN) and request written permission to remove findings from work area; and</li> <li>○ Recovery, packaging and labelling of findings for transfer to National Museum.</li> <li>● Should human remains be found, the following actions will be required:             <ul style="list-style-type: none"> <li>○ Apply the chance find procedure as described above;</li> <li>○ Schedule a field inspection with an archaeologist to confirm that remains are human;</li> <li>○ Advise and liaise with the NHCN and Police; and</li> <li>○ Remains will be recovered and removed either to the National Museum or the National Forensic Laboratory.</li> </ul> </li> </ul>	



**4.5 OPERATION AND MAINTENANCE PHASE**

The management actions included in **Table 4-4** below apply during the operation and maintenance phase of these developments.

**Table 4-4: Operation and maintenance management actions**

<b>Environmental Feature</b>	<b>Impact</b>	<b>Management Actions</b>	<b>Person Responsible</b>
EMP training	Lack of EMP awareness and the implications thereof	All contractors appointed for maintenance work on the respective streets must ensure that all personnel are aware of necessary health, safety and environmental considerations applicable to their respective work.	Contractor
Water	Surface and groundwater contamination	Ensure that surface run-off water accumulating on-site are channeled and captured through a proper storm water management system to be treated in an appropriate manner before disposal into the environment.	Proponent, Contractor,
Aesthetics	Visual impacts	<p>The proponent should consult with a view to incorporate the relevant local/national/international development guidelines which addresses the following:</p> <ul style="list-style-type: none"> <li>• The incorporation of indigenous vegetation into the development.</li> <li>• To mark the area with appropriate road warning signs (e.g. the road curves to the left/right)</li> <li>• ‘green’ technologies should be implemented within the architectural designs and building materials of the development where possible to minimize the visual prominence of such a development within the more natural surrounding landscape.</li> </ul>	Proponent

Environmental Feature	Impact	Management Actions	Person Responsible
		<ul style="list-style-type: none"> <li>• keep existing trees, introduce tall indigenous trees; keep structures unpainted and minimizing large advertising billboards.</li> <li>• No illegal dumping of waste should be allowed.</li> </ul>	
Noise	Nuisance impacts	<p>No activity having a potential noise impact should be allowed after 18:00 hours if possible.</p> <ul style="list-style-type: none"> <li>• Do not allow commercial activities that generate excessive noise levels.</li> <li>• Continuous monitoring of noise levels should be conducted to make sure the noise levels does not exceed acceptable limits.</li> </ul>	Proponent
Socio-Economic	Social Impacts	<p>The local community be consulted in terms of possible job creation opportunities and must be given priority if unspecialised job vacancies are available.</p>	Proponent

**4.6 DECOMMISSIONING PHASE**

The decommissioning of these developments is not foreseen as the intended development is envisaged to be permanent. If this infrastructure development is decommissioned the following management actions should apply.

**Table 4-5: Decommissioning phase management actions**

<b>Environmental Feature</b>	<b>Management Actions</b>
Decommissioning activity	Many of the mitigation measures prescribed for construction activity for these developments ( <b>Table 4-3</b> above) would be applicable to some of the decommissioning activities. These should be adhered to where applicable.

**5 CONCLUSION**

The management actions included in this report aim to assist in the avoidance, management and/or mitigation of potential impacts on the environment that may result from the proposed activities.

Should the measures recommended in this EMP be implemented and monitored, SPC is confident that the risks identified in the FESR can be reduced to acceptable levels.
